

BANGLADESH WATER DEVELOPMENT BOARD



Project Completion Report: IMED 04/2024

Name of the Project : Protection from the erosion of Jamuna River at Pakerdaha & Balijuri of Madargonj Upazila of Jamalpur district and at Jamthal of Sariakandi Upazila of Bogra district (1st Revised).

Implementation Period : April, 2020 to June, 2025

October 2025

Government of the People's Republic of Bangladesh
Ministry of planning
Implementation Monitoring and Evaluation Division

PROJECT COMPLETION REPORT (PCR): IMED 04/2024 (Revised)

A. PROJECT DESCRIPTION

- 01. Name of the Project** : Protection from the erosion of Jamuna River at Pakerdaha & Balijuri of Madargonj Upazila of Jamalpur district and at Jamthal of Sariakandi Upazila of Bogra district (1st Revised)
- 02. Administrative Ministry/Division** : Ministry of Water Resources (MoWR).
- 03. Executing Agency** : Bangladesh Water Development Board (BWDB).
- 04. Planning Commission Sector/Division** :
- 05. Type of Project (Investment/Technical/Feasibility Study):** Investment
- 06. Location of the Project (As per Project Document):**

Sl. No	Division	District	City Corporation/ Municipality/Upazila
1.	Mymensingh	Jamalpur	Madargonj.
2.	Rajshahi	Bogra	Sariakandi

07. Estimated Cost, Implementation Period and Approval:

(In Lakh Taka)

Subject	Approved Estimated Cost				Implementation Period	Date of Approval	Approved by
	Total	GOB (Foreign Exchange)	PA (RPA)	Self-financ e			
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)
Original	58472.24	58472.24 (0.00)	-	-	April,2020 to June 2023	10/03/2020	ECNEC
1 st Revised	57441.00	57441.00 (0.00)	-	-	April,2020 to June 2024	23/05/2023	MoWR
2 nd Revised (Economic Code Correction)	57441.00	57441.00 (0.00)	-	-	April,2020 to June 2024	24/01/2024	MoWR
1 st No Cost Extension	57441.00	57441.00 (0.00)	-	-	April,2020 to June 2025	01/08/2024	Planning Commision
2 nd No Cost Extension (If Applicable)	-	-	-	-	-	-	-
Intercomponent Adjustment (If applicable)	-	-	-	-	-	-	-

08. Objective of the Project

Overall objective:

To stop Jamuna River bank erosion by implementation of permanent protective works of length 6.75 Km. along with two end termination at upstream and downstream, along the left bank of Jamuna river at pakerdah and Balijuri of Madargonj upazila of Jamalpur district and at Jamthal area of Sariakandi upazila of Bogura district.

Specific Objectives (in bullets):

- To arrest river bank erosion of approximately 2000 ha area by construction of River Bank Protection works for a length of 6.75 km.;
- To protect Balijuri and Pakerdah union of Jamalpur district and Jamthal area under Sariakandi Upazila of Bogura district from erosion of the Jamuna River and thereby save various government and non-government educational institutions, religious establishments, agricultural land, crops, houses, etc. costing approximately Tk. 231125.00 lakh;
- To improve the socio-economic condition of the project area and resist the adverse impact of the national economy;
- To reduce poverty and create opportunities for employment.

09. Background of the Project (In brief):

River erosion of major river in Bangladesh is a major problem and has a severe negative impact on the livelihoods of people living along the riverbanks. While normal flooding is beneficial for agriculture and fish production, the widening of rivers due to erosion threatens highly productive agricultural lands and settlements, including critical infrastructure. This type of natural problems raises increasingly due to climate changes affect and it's taking a deadly shape. Uncontrolled and increasing river erosion phenomenon made damages to the important infrastructures as well as unexpected severe flood also damages crops, agriculture and various infrastructures. As a result, investment in various sector faces interruptions and fertile agricultural land losses it's productivity.

Main problem and challenges of the river Jamuna is its frequent changes of the channel morphology. River bed of the Jamuna River had made with fine unstable mica and erodible silt-sand which made the characteristics of the river morphology very unstable and couldn't make a steady and stable river bed like other natural rivers. About in every rainy season, the Jamuna River made a new flowing channel and also made a flowing channel abandon. Therefore, in the boundary of the River Jamuna i.e. within the both bank of the Jamuna River, there are two or more flowing channel exists, which makes the river system as a braided river. Henceforth, there is an unstable flowing channel and uncertain erosion pattern always exists along the Jamuna River banks. On the other hand, Jamuna River is the heist silt carrying flowing natural river all over the world. The carrying silt deposited in various places within the river boundary which makes several sand bars. In every year, these sand bars increase in size and numbers within the river boundary which may causes bank erosion in various places along the river banks.

Kajla union of Sariakandi upazila of Bogra district and Pakerdah & Balijuri union of Madargonj upazila of Jamalpur district situated on the left bank of Jamuna River. Jamalpur district is one of the poorest districts of Bangladesh and therefore, government of Bangladesh planned to implement various development project in this district during the last ten to fifteen years, so that socio-economic condition of peoples can improved fast. Google Map of this madargonj area during the last ten years, shows frequent river bank erosion occurred and made the river bank shifted towards country side. On the other hand, sand bars within the river bed increase its size every year which may cause the river flow changes to oblique flow hits the river bank finally causing river bank erosion. During the last few years, this oblique flow pattern made severe river bank erosion in the above mentioned Kajla, Pakerdah and Balijuri union area.

Furthermore, a 200 megawatt solar power plant, Jute research sub-center and Jute textile complex was under construction, are situated within the two kilometer in that area. The terretory of the area between the upazila headquarter and the Jute textile complex and the other under construction infrastructures is lower in nature and there are few numbers of khals flowing. The 200 mega watt solar power plant construction was ongoing in that area, where the low land was filled up to the ground level. Therefore, if the river bank erosion was going on as well, the under-construction infrastructures may fallen in threaten to damages or disappear due to river erosion. The Sarishabari upazila situated at the left bank of Jamuna River at the down stream area of Madargonj upazila, also may fall in threat of Jamuna River Bank erosion.

It is noteworthy that, during 1980-85 one of the channels of the Jamuna River was flowing through the Madargonj Upazila, which was shifted towards west duing the last fifteen to tewenty years of time. A few parts of that channel now-a-days became beel or pond used by the local people for fisheries and agriculture purposes. The morphological behaviour of the Jamuna River was not like a threat for further erosion in that area for last thirty years but now-a-days it became harmfull as the rate of river bank erosion was increases time to time particularly in that area as described above. A trust of Water Resources ministry, the CEGIS had been made a report "Prediction of river erosion along the Jamuna, the Ganges and the Padma Rivers in 2015" described the prediction of severe river bank erosion at Balijuri & Pakerdaha area of Madargonj upazila of Jamalpur district and at Jamthal area of Sariakandi upazila of Bogra district. Practically, the river bank erosion was started in that area and if this type of erosion was going on, the entire area may fall in to a natural disasterous situation. The socio-economic condition of the people of that area may threatened by the loss of river bank erosion.

7/3/22

10. Major Activities:

Physical Work	Location	Length	Estimated Cost (Lakh Tk.)
i) Permanent Protective Work	Pakerdaha and Balijuri of Madargonj Upazila and Jamthal area of Sariakandi Upazila	6.75 Km.	49640.91
ii) End Termination	Do	2 Nos.	7568.09

11. Reasons for Revision (if applicable):

- **1st Revision:**

The project was approved by the ECNEC on 10-04-2020 with a project implementation period from April 2020 to June 2023. But the physical work starts from July 2021. After starting the physical works, at the downstream of the project area, the river morphological changes occurred and a new area was affected by the bank erosion. Regarding the issue, project implementing authority submit a short report to the ministry of water resources. Ministry instruct the BWDB to form a technical committee to visit the newly developed erosion prone area at downstream of the project area and also to submit a detail report regarding the issue including their recommendation. Accordingly, the technical committee prepare a detail report after visiting the area with their recommendation. Therefore, project revision was needful to address the project vulnerability along with the new erosion prone area at downstream of the project area.

- **2nd Revision**

Economic Code of one revenue item changed by finance ministry during the implementation of iBas++ system for development project bill payment. Therefore, the DPP of the project need to revised to replace the new economic code of the item in the RDPP.

11.1 Reasons for No-Cost Time Extension (if applicable):

- **1st time No-Cost Time Extension**

The project was categorized as "B-Category" development project by finance division after the Covid-19 as to mitigate the post effect of Corona pandemic. As a B-Category development project, it had to receive inadequate budget allocation during the first three years of the implementation period. Therefore, finally one year extension of implementation period was required to complete the physical work of the project.

- **2nd time No-Cost Time Extension**
Not Applicable

12. Financing Arrangement (Source-wise):**12.1 Status of Loan/Grant****a) Foreign Financing:**

Source (s)	Currency as per Agreement	Amount in US\$ (million)	Nature (Loan/Grant/supplier's credit)	Date of Agreement	Date of Effectiveness	Date of Closing	
						Original	Revised
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)
-----N/A-----							

b) GOB:

Total amount	Loan	Grant	Cash Foreign Exchange
(1)	(2)	(3)	(4)
57441.00	-	57441.00	-

c) Self-finance/Equity:

Total amount	Self-finance	Equity	Cash Foreign Exchange
(1)	(2)	(3)	(4)
-----N/A-----			

12.2 Utilization of Project Aid (Source wise):

Source (s)	Total Amount		Actual Expenditure		Unutilized Amount	
	In Us\$	In Local Currency	In Us\$	In Local Currency	In Us\$	In Local Currency
(1)	(2)	(3)	(4)	(5)	(6)	(7)
-----N/A-----						

12.3 Reimbursable project Aid (RPA):

Source (s)	RPA Amount		Amount	Amount	Amount	Remarks
	As per Project Document	As per Agreement	Spent	Claimed	Re-imbrued	
(1)	(2)	(3)	(4)	(5)	(6)	(7)
-----N/A-----						

B. IMPLEMENTATION POSITION

13. Implementation Period:

Implementation Period as per Project Document		Actual implementation	Time Over-run (% of original implementation period)	Remarks
Original	Latest Revised			
(1)	(2)	(3)	(4)	(5)
April/2020 to June/2023	April/2020 to June/2025	April/2020 to June/2025	2 years (61.69%)	Although the project implementation period starts from April, 2020 as per the approved DPP of the project, actually implementation period starts from July 2020 and ADP budget allocation received from the FY 2020-21. Also, after starting the implantation of the project, Jamuna River morphological changes observed in the project area and the issue was reported properly to the competent authority. A technical committee was formed to address the issue regarding the river morphological changes. The technical committee visit the project area and made recommendation to include extra 0.50 Km protective works and to exclude the Jamuna River dredging from the approved DPP of the project. Accordingly, the project DPP had been revised as per the recommendation of the technical committee. During this revision of the DPP, implementation period was increased by one year. Also, the project was categorized as "B-Category" development project by finance division after the Covid-19 as to mitigate the post affect of Corona pandemic. As a B-Category development project, it had to receive inadequate budget allocation during the first three years of the implementation period. Therefore, one year extension of the implementation period required for completion of the physical works fully.

14. Cost of the Project:

Description	Estimated Cost		Actual expenditure	Cost over-run (% of original cost)	Remarks
	Original	Latest revised			
(1)	(2)	(3)	(4)	(5)	(6)
TOTAL TAKA (Lakh)	58472.24	57441.00	49502.17	-15.34%	Due to the less in quoted price of the contractors participate in the procurement process and also final bill of six contracts were about 9% lesser than the contract prices as per the actual implementation, the cost of the whole project decreased by 15.34%

BSR

15. Information regarding Project Director (s):

Name, Main Designation & Grade. Mobile Number (From Beginning)	Full time (Yes/No)	Part time (Yes/No)	Responsible for more than one project	Period		Remarks
				Joining	Transfer	
(1)	(2)	(3)	(4)	(5)	(6)	(7)
Md. Shahjahan Siraj Superintending Engineer Pay Scale: 4 th Grade BDT 50,000 - 71200/-	Yes	No	Yes	20 August, 2020	11 October, 2021	
Md. Mahfuzur Rahman Superintending Engineer Pay Scale: 4 th Grade BDT 50,000 - 71200/-	Yes	No	Yes	11 October, 2021	27 June, 2022	
Md. Sirajul Islam Superintending Engineer Pay Scale: 4 th Grade BDT 50,000 - 71200/-	Yes	No	No	27 June, 2022	30 June, 2025	

16. Personnel:

16.1 Personnel of Project implementation Unit (PIU):

Sl. No.	Name of Post (Grade)	Approved Strength	Employed during Implementation
(1)	(2)	(3)	(4)
1	Officers	Implementation of the project was done by the existing manpower of the implementing agency.	
2	Staffs		
Total=			

16.2 Personnel Required after the Project Completion:

Sl. No.	As Proposed in Project Document (PD)		Recruited (Yes/No)	If not recruited explain reason and latest status
	Name of Post	Number		
(1)	(2)	(3)	(4)	(5)
-----N/A-----				
Total=				

*After completion of the project regular monitoring will be done by Jamalpur Water Development Division by its permanent manpower.

17. Training (Foreign/Local):

Category	Sl. No.	No. of Days/Weeks/Months (D/W/M), Batch & Participants					
		As in Project Document			Achievement		
		D/W/M	Batch (s)	Participants(s)	D/W/M	Batch (s)	Participants(s)
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)
Local Training	-----N/A-----						
Sub Total=							
Foreign Training	-----N/A-----						
Sub Total=							
Total=							

(PD= Project Document)

[Signature]

18. Component-wise Progress (As per latest approved Project Document):

Name of Component	Unit	Quantity	Estimated Cost (Taka in Lac)					Actual Progress (Taka in Lac)				
			Total	GOB	PA	Self-finance	Others	Total	GOB	PA	Self-finance	Others
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)
(a) Revenue:												
Honorarium for Mid-Term Evaluation	L.S.	1 item	10.00	10.00	-	-	-	9.95	9.95	-	-	-
Honorarium for PSC, PIC, TEC, etc. members	L.S.	1 item	10.00	10.00	-	-	-	9.07	9.07	-	-	-
Travel allowance	L.S.	1 item	3.00	3.00	-	-	-	2.17	2.17	-	-	-
Petrol & Lubricant	L.S.	1 item	10.00	10.00	-	-	-	8.595	8.595	-	-	-
Printing & Publications	L.S.	1 item	2.00	2.00	-	-	-	2.00	2.00	-	-	-
Stationary, seal & stamps	L.S.	1 item	2.00	2.00	-	-	-	1.75	1.75	-	-	-
Computer & photocopies Consumables	L.S.	1 item	2.00	2.00	-	-	-	2.00	2.00	-	-	-
Survey (Bathymetry and Bank line Survey)	L.S.	1 item	17.00	17.00	-	-	-	16.94	16.94	-	-	-
Repair of existing Transport & Vehicle (4 nos. Jeep & 6 Nos. motorcycle)	L.S.	1 item	5.00	5.00	-	-	-	4.97	4.97	-	-	-
Repair of Computer & Office equipment	L.S.	1 item	2.00	2.00	-	-	-	1.99	1.99	-	-	-
Sub-total (Revenue) =			63.00	63.00	-	-	-	59.44	59.44	-	-	-
(b) Capital												
Jeep (5-doors, Not exceeding 2500 CC)	Nos.	1	61.00	61.00	-	-	-	61.00	61.00	-	-	-
Photocopier	Nos.	1	1.50	1.50	-	-	-	1.50	1.50	-	-	-
Computers (Printer & Scanners)	Nos.	3	2.50	2.50	-	-	-	2.50	2.50	-	-	-
Office Furniture	L.S.	1 item	2.00	2.00	-	-	-	2.00	2.00	-	-	-
Tree Plantation	L. S.	1 item	2.00	2.00	-	-	-	2.00	2.00	-	-	-

Name of Component	Unit	Quantity	Estimated Cost (Taka in Lac)					Actual Progress (Taka in Lac)				
			Total	GOB	PA	Self-finance	Others	Total	GOB	PA	Self-finance	Others
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)
Protective Work along the left bank of Jamuna River from km 0.00 to km 6.75 = 6.75 km	Km.	6.75	49640.91	49640.91	-	-	-	43577.54	43577.54	-	-	-
Construction of U/S End Termination at Km. 0.00 (length of 523.04m) and D/S End Termination at Km. 6.25 (length 128.00m)	Nos.	2	7568.09	7568.09	-	-	-	5796.19	5796.19	-	-	-
Sub-total (Capital)			57278.00	57278.00	-	-	-	49442.73	49442.73	-	-	-
Total a+b (Revenue + Capital)			57441.00	57441.00				49502.17	49502.17			

19. Procurement of Transport (in Nos.):

Type of transport	Number as per Project Document	Number Procured with date	Transferred to Transport Pool with date	Transferred to O & M with date	Condemned/damaged with date	Returned or transferred to following project	Remarks
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)
Car							
Jeep	1	1	-	-	-	-	Necessary Action has been taken as per memo no. 2549, date: 20-07-2025 of Project Director office
Microbus	-	-	-	-	-	-	
Minibus	-	-	-	-	-	-	
Bus	-	-	-	-	-	-	
Pick-up	-	-	-	-	-	-	
Truck	-	-	-	-	-	-	
Motor -Cycle	-	-	-	-	-	-	
By-cycle	-	-	-	-	-	-	
Speed Boat	-	-	-	-	-	-	
Launch	-	-	-	-	-	-	

[Signature]

20. Project Consultant (s) (Local/Foreign):

Name of the Field	Approved man month		Actual man month utilized	Number of Deliverables		Remarks
	As per Project Document	As per contract		As per Project Document	Actual	
(1)	(2)	(3)	(4)	(5)	(6)	(7)
a) Local:	-----N/A-----					
b) Foreign:	-----N/A-----					

21. Infrastructure/Erection/Installation Tools & Equipment: (Photocopier, Computer and Office Furniture)

Description	Quantity (as per project document)	Quantity Procured with date	Transferred to O & M with date	Disposed-off as per rule with date	Balance	Remarks
(1)	(2)	(3)	(4)	(5)	(6)	(7)
Photocopier	1	1 28/06/2021				Necessary Action has been taken as per memo no. 2549, date: 20-07-2025 of Project Director office
Computer	1 computer 1 laser printer and 1 scanner	1 28/06/2021				
Office Furniture	One Set	One Set 29/06/2022				

22. Procurement of Goods, Works and Services:

22.1 Information on packages:

- a) Total number of packages as per Project Document: **29 Nos.** (Goods -**04 Nos.**; Works -**25 Nos.**; Services- 0 No.)
- b) Total number of packages procured: **29 Nos.** (Goods- **04 Nos.**; Works- **25 Nos.**; Services- 0 No.)
- c) Reason for not procuring (if any): N/A
- d) Number of packages for which the estimated cost is more than 1% of the estimated cost of the project: N/A (Goods- 0 No.; Works- 0 No.; Services- 0 No.)

22.2 Detailed Package-wise information of Goods, Works and Services (For each case the highest 50 (fifty) packages) (Please use the format as in Annexure-I (a), I(b) and I(c))

C. FINANCIAL AND PHYSICAL TARGET AND PROGRESS

23. Original and Revised Financial Provision and physical Target (as per Project Document):

Financial Year	Financial provision & physical target as per original Project Document						Financial provision & physical target as per latest revised Project Document					
	Total	GOB	P. A	Self-finance	Others	Physical %	Total	GOB	P. A	Self-finance	Others	Physical %
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)
2019-20	102.10	102.10	-	-	-	0.00%	0.00	0.00	-	-	-	0.00%
2020-21	14265.30	14265.30	-	-	-	2.10%	1704.04	1704.04	-	-	-	15.87%
2021-22	30440.52	30440.52	-	-	-	30.66%	6455.61	6455.61	-	-	-	1.35%

BSM

Financial Year	Financial provision & physical target as per original Project Document						Financial provision & physical target as per latest revised Project Document					
	Total	GOB	P. A	Self-finance	Others	Physical %	Total	GOB	P. A	Self-finance	Others	Physical %
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)
2022-23	13664.32	13664.32	-	-	-	49.30%	19520.92	19520.92	-	-	-	3.84%
2023-24	0.00	0.00	-	-	-	17.89%	29760.43	29760.43	-	-	-	2.59%
2024-25	0.00	0.00	-	-	-	-	0.00	0.00	-	-	-	2.02%
	58472.24	58472.24	-	-	-	100.00%	57441.00	57441.00	-	-	-	100.00%

24. Revised ADP allocation and progress:

Financial Year	Revised Allocation & target						GOB Release	Expenditure & physical progress						Unspent * GoB Released
	Total	GOB	P. A.	Self-Finance	Others	Physical %		Total	GOB	P. A.	Self-Finance	Others	Physical %	
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)	(14)	(15) = 8-10
2019-20	0.00	0.00				0.00%	0.00	0.00	0.00				0.00%	
2020-21	1800.00	1800.00				18.00%	1800.00	1704.04	1704.04				15.87%	
2021-22	6500.00	6500.00				32.00%	6500.00	6455.61	6455.61				24.89%	
2022-23	21852.00	21852.00				27.00%	15999.25	15998.70	15998.70				27.00%	
2023-24	16000.00	16000.00				20.00%	15999.00	15997.20	15997.20				20.00%	
2024-25	10200.00	10200.00				12.24%	10200.00	9346.62	9346.62				10.32%	
Total =	56352.00	56352.00				109.24%	50498.25	49502.17	49502.17				98.08%	

* Attach the Proof for Reconciliation of Unspent GOB Released

** To determine the physical quantity, use the formula as in the circular of Planning Division

BR

D. ACHIEVEMENT OF OBJECTIVES OF THE PROJECT

25. Project objective, Actual achievement and Reason for shortfall (if any):

Objectives as per DPP	Actual achievement	Reasons for shortfall, if any
(a) To arrest river bank erosion of approximately 2000 ha area by construction of River Bank Protection works for a length of 6.25 km.;	(a) River bank erosion has been stopped permanently by implementing 6.75 km permanent protective works along the left bank of Jamuna River at Pakerdaha & Balijuri area of Madargonj upazila of Jamalpur district and at Jamthal area of Sariakandi upazila of Bogra district.	No shortfall exists
(b) To protect Balijuri and Pakerdah union of Jamalpur district and Jamthal area under Sariakandi Upazila of Bogura district from erosion of the Jamuna River and thereby save various government and non-government educational institutions, religious establishments, agricultural land, crops, houses, etc. costing approximately Tk. 231125.00 lakh;	(b) Various government and non-government educational institutions, religious establishments, agricultural land, crops, houses, etc. of valued approximately 231125.00 lakh BDT has been saved from the erosion of the Jamuna River by implementing permanent protective works of length 6.75 km. along the left bank of Jamuna River at Balijuri and Pakerdah union of Jamalpur district and Jamthal area under Sariakandi Upazila of Bogura district	Yearly adequate operation & maintenance budget will require to remain the protective works performing to protect against river erosion.
(c) To improve the socio-economic condition of the project area and resist the adverse impact of the national economy;	(c) River bank erosion has been stopped permanently due to the implementation of permanent protective works in the project area. This will make the local people confident to construct their permanent residence and also will make them comfortable to do their regular socio-economic activities without feeling any uncertainty. This will improve the socio-economic condition of the project area and will obviously resist the adverse impact of the national economy.	
(d) To reduce poverty and create opportunities for employment	(d) Loss of residence, agricultural land, crops, livestock and livelihood etc will reduce poverty and regular business activities will definitely create employment opportunities in the project area	

JSR

E. BENEFIT ANALYSIS

26. Annual Out-put:

Items of out-put	Unit	Estimated quantity expected at full capacity	Actual quantity of out-put during the 1 st year of operation at full capacity (or during, real production for newly completed project)
a) Agriculture/Paddy Production	Mt.	9440.00	9440.00
b) Business growth of local people	Item	1 item	1 item
c) Environmental Recovery	Item	1 item	1 item

27. Cost/Benefit:

Item	Estimated	Actual
(1) Benefit cost ratio of the project:	(1) B/C Ratio	Will be evaluated later by concern directorate of BWDB & IMED.
(i) Financial	(i) 1.35: 1	
(ii) Economic	(ii) 1.55: 1	
(2) Internal Rate of Return:	(2) Internal Rate of Return	
(i) Financial	(i) 17.90%	
(ii) Economic	(ii) 20.74%	

28. Please give reasons for shortfall, if any, between the estimated and actual benefit: N/A

F. MONITORING AND AUDITING

29. Monitoring:

JSK

Name & designation of the inspecting official	Date of Inspection	Identified Problems	Recommendations
1	2	3	4
(a) IMED: i) Mr. Mohammad Shawkat Ali, Director, Sector-4, IMED	07-06-2024	Not Found	i) The Physical Progress of the Project is 85.68% upto May, 2024 and financial progress is 62.31%. Out of 25 packages for 6.75 Km. protective works and 2nos. end termination, the physical works of 11 nos. packages had completed and 14 nos. of packages works were on-going. Due to the upcoming rainy season, the remaining works could not be started before next November. Therefore, one year time extension of the project implementation period will necessary and it may consider. ii) The physical works of the project should be implemented following approved design and specifications. iii) The completion of the project work should be ensured during the proposed extended time and therefore, necessary fund release should be ensured and monitoring should be strengthened for these purposes. Necessary action should be taken for the resolution of the audit objection arises for this project expenditure.
(b) Ministry			
1. Kabir Bin Anwar Senior Secretary Ministry of Water Resources	14-11-2021	Not Found	i) Physical works of that packages at site not yet started, should be start immediately without any delay. ii) The C.C. blocks manufacturing should be start as fast as possible which are required to construct the permanent protective works. iii) Invitation of tender should be published immediately to implement the rest 1.90 km protective works and the 2 nos. end termination at project area. iv) At the downstream of the project area, the unprotected river bank starts to eroded recently, should be included in the project by the recommendation of the technical committee and also the necessity of dredging works should be assessed needfully in the project area.

JSR

Name & designation of the inspecting official	Date of Inspection	Identified Problems	Recommendations
1	2	3	4
3. Mr. Mohammad Mobashsherul Islam, Deputy Secretary, Planning-3, MoWR	29-08-2021	The project has outstanding bill of 93.00 crore taka during the last financial year. This year allocation is only 50 crore, which is insufficient. Therefore, additional allocation will necessary to complete the project work in time.	The project work should be implemented with maintaining the quality of the physical work. Jamalpur BWDB Division sufferings from the insufficiency of vehicle in order to visit the erosion prone vulnerable area of Jamalpur district which is situated on the left bank of Jamuna River. Board should have necessary action to provide vehicles to this field office in order to run the supervision of the works and to do the other needful duty.
4. i) Mr. S. M Rezaul Mostafa Kamal, Addl Secretary (planning), MoWR, Dhaka. ii) Joint Secretary, Ministry of Finance, Dhaka	11-06-2022	Not Found	The team visited the project in order monitor the implementation status of the all component of the project as mid-term evaluation of the project.
5. Mr. Md. Abdullah Al Arif, Joint Secretary, MoWR	09-06-2025	Not Found	i) Executive Engineer, Jamalpur WD Division inform that there are 25 nos. of packages to implement the project work. Among the 25 packages already 18 nos. of packages physical work had been completed and the other 7 nos. of packages works are on-going and they will also be completed within June, 2025. ii) During the visit, the work quality is found satisfactory and the work has been completed as per approved design and specifications. iii) The remaining seven packages of works should be completed as per the design and specifications within the stipulated time.
Agency:			
1. Mr. Md. Abdul Matin Sarker, Chief Engineer, Central Zone, BWDB, Dhaka.	07-10-2021	Not Found	1. Physical works of the project should be started just after the monsoon with maintaining quality of the works. 2. The technical committee formed by board will visit the project site soon and will made recommendation for further action. Field office should follow the recommendation of the technical committee.
2. Mr. Md. Rafiqul Islam Chaubey, Chief Engineer (Monitoring), BWDB, Dhaka	04-12-2021	Not Found	1. Construction materials reserve at site should adequate so that by increasing labour progress of C.C. blocks manufacturing can be increased. 2. The steel shutters for manufacturing C. C. blocks should be at proper size and shape. 3. For the better progress of the whole project, the remaining 10 packages for 1.90 km. protective works tender should be invited during this dry season.

Name & designation of the inspecting official	Date of Inspection	Identified Problems	Recommendations
3. i) Mr. Enayet Ullah, Additional Director General (Eastern Region), BWDB, Dhaka. ii) Mr. Md. Asaduzzaman, Chief Engineer, Central Zone, BWDB, Dhaka.	08-09- 2023	Silt deposited on the launching apron made by partial dumping of geo-bags.	The deposited silt on the launching apron should be removed properly before further dumping of geo-bags starting during this working season. The combination of C. C. blocks and Geo-bags should be as per the approved design and this will be ensured by the Executive Engineer. During the visit, the Jamuna River was full of water flow. Therefore, during this time, construction material carrying at site should be easier than dry season carriage by road. The contractors should be inspired by project officials to carrying materials at site by river route. The Pro-rata progress should be ensured by the contractors with time elapsed.
4. i) Mr. Md. Amirul Haque Bhuiyan, Addl DG (Eastern Region), BWDB, Dhaka ii) Mr. Md. Asaduzzaman Chief Engineer, Central Zone, BWDB, Dhaka.		Not Found	The material mobilization at site is satisfactory for 10 nos. of packages as found during the site visit. The quality of the C. C. block construction and also progress of works must be ensured as per the approved design and specification.
5. i) Mr. Md. Moniruzzaman, Adll Director General (East Region), BWDB, Dhaka. ii) Mr. Md. Asaduzzaman, Chief Engineer, Central Zone, BWDB, Dhaka.		Not Found	The overall progress of the protective work should be achieved as pro-rata basis. The quality of the C. C. block construction must be ensured as per the specification.
6. Mr. Md. Rafius Sazzad Pengg, Chief Engineer, Central Zone, BWDB, Dhaka.	11-06- 2025	Not Found	The physical progress of six packages are not satisfactory. During the working period, the contractors of that six packages were instructed and requested several times verbally and by written. But they didn't comply with. Finally, they are instructed to mobilize necessary materials and increase labour for finishing the physical works within next seven to ten days. Though, the project implementation period will ended within the June, 2025, the contractors will punished as per the contract agreement if they failed to complete the whole works as per approved design and specifications.
7. Mr. Md. Sirajul Islam Superintending Engineer Tangail WD Circle, BWDB, Tangail and Project Director	Several Times	Not Found	The quality of the C. C. block construction and also progress of works must be ensured
(c) Others: (Please specify)			

732

30. Auditing during and after Implementation:**30.1 Internal Audit:**

Period of Audit	Date of submission of Audit Report	Sl. No.	Major findings/objections and Money involved	Whether objections resolved or not (if not, mention status)
1	2	3	4	5
-----N/A-----				
Total findings/objections and Money involved=				

30.2 External Audit:

Period of Audit	Date of submission of Audit Report	Sl. No.	Major findings/objections and Money involved	Whether objections resolved or not (if not, mention status)
1	2	3	4	5
2019-2022	10-02-2023	18	By the violation of the instructions of the Finance Ministry, in purchase of a Vehicle the irregular expenses of BDT 5,80,000.00 occurred.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2019-2022	10-02-2023	08	In accordance with the clause of the contract agreement, the insurance of Risk on contract works did not file, for which a loss of BDT 36,74,121 had been occurred from the VAT on premium of the insurance.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2022-2023	11-10-2023	04	An irregular expense of BDT 52,80,351 had been occurred due to made payment on a bill of C.C. blocks without performing quality check by testing standard quality.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2022-2023	11-10-2023	01	In accordance with the clause of the contract agreement, the insurance of Risk on contract works did not file, for which a loss of BDT 5,49,200 had been occurred from the VAT on premium of the insurance.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2022-2023	11-10-2023	02	The making of BOQ with excess unit rate than the estimate made by rate schedule, loss of board of BDT 1,71,622.00 had been occurred.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2022-2023	11-10-2023	03	The contractor fails to complete the works implementation with in the stipulated time, needs to fine as liquidated damage of amount 58,77,328.00 which will be treated as revenue loss of Board.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2023-2024	05-12-2024	04	Work completed by low quality and out of specification C. C. blocks, a financial loss of board occurred of amounting BDT 5,46,035.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2023-2024	05-12-2024	01	In accordance with the clause of the contract agreement, the insurance of Risk on contract works did not file, for which a loss of BDT 32,02,743.00 had	A Brod-sheet reply already had been submitted along with the necessary evidences.

Period of Audit	Date of submission of Audit Report	Sl. No.	Major findings/objections and Money involved	Whether objections resolved or not (if not, mention status)
1	2	3	4	5
			been occurred from the VAT on premium of the insurance.	Not yet resolved.
2023-2024	05-12-2024	05	Payment of excess bill of C. C. blocks with a quantity larger than the quantity certified by the Task force, a loss of amounting 10,34,060 taka had been occurred.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
2023-2024	05-12-2024	02	Completion of works and made payment of bills without following the instruction of approved design, a loss of board occurred amounting BDT 62,26,350.	A Brod-sheet reply already had been submitted along with the necessary evidences. Not yet resolved.
Total findings/objections and Money involved=				

Br

(b) POST-PROJECT REMARKS

31. General Observations/Remarks on the Project

31.1 Background

River erosion of major river in Bangladesh is a major problem and has a severe negative impact on the livelihoods of people living along the riverbanks. While normal flooding is beneficial for agriculture and fish production, the widening of rivers due to erosion threatens highly productive agricultural lands and settlements, including critical infrastructure. This type of natural problems raises increasingly due to climate changes affect and it's taking a deadly shape. Uncontrolled and increasing river erosion phenomenon made damages to the important infrastructures as well as unexpected severe flood also damages crops, agriculture and various infrastructures. As a result, investment in various sector faces interruptions and fertile agricultural land losses it's productivity.

Main problem and challenges of the river Jamuna is its frequent changes of the channel morphology. River bed of the Jamuna River had made with fine unstable mica and erodible silt-sand which made the characteristics of the river morphology very unstable and couldn't make a steady and stable river bed like other natural rivers. About in every rainy season, the Jamuna River made a new flowing channel and also made a flowing channel abandon. Therefore, in the boundary of the River Jamuna i.e. within the both bank of the Jamuna River, there are two or more flowing channel exists, which makes the river system as a braided river. Henceforth, there is an unstable flowing channel and uncertain erosion pattern always exists along the Jamuna River banks. On the other hand, Jamuna River is the heist silt carrying flowing natural river all over the world. The carrying silt deposited in various places within the river boundary which makes several sand bars. In every year, these sand bars increase in size and numbers within the river boundary which may causes bank erosion in various places along the river banks.

Kajla union of Sariakandi upazila of Bogra district and Pakerdah & Balijuri union of Madargonj upazila of Jamalpur district situated on the left bank of Jamuna River. Jamalpur district is one of the poorest districts of Bangladesh and therefore, government of Bangladesh planned to implement various development project in this district during the last ten to fifteen years, so that socio-economic condition of peoples can improved fast. Google Map of this madargonj area during the last ten years, shows frequent river bank erosion occurred and made the river bank shifted towards country side. On the other hand, sand bars within the river bed increase its size every year which may cause the river flow changes to oblique flow hits the river bank finally causing river bank erosion. During the last few years, this oblique flow pattern made severe river bank erosion in the above mentioned Kajla, Pakerdah and Balijuri union area.

Mr. Mirza Azam, the honorable state minister, ministry of Jute and textile, peoples republic of Bangladesh sent a demi-official letter to the honorable state minister, Ministry of Water Resources, peoples republic of Bangladesh, requesting to formulate and implement a development project in order to prevent the river bank erosion of the left bank of Jamuna River at Madargonj and Sariakandi upazila of Jamalpur and Bogra district respectively. Furthermore, a 200 megawatt solar power plant, Jute research sub-center and Jute textile complex was under construction, are situated within the two kilometer in that area. The territory of the area between the upazila headquarter and the Jute textile complex and the other under construction



infrastructures is lower in nature and there are few numbers of khals flowing. The 200 megawatt solar power plant construction was ongoing in that area, where the low land was filled up to the ground level. Therefore, if the river bank erosion was going on as well, the under-construction infrastructures may fall in threaten to damages or disappear due to river erosion. The Sarishabari upazila situated at the left bank of Jamuna River at the downstream area of Madargonj upazila, also may fall in threat of Jamuna River Bank erosion.

It is noteworthy that, during 1980-85 one of the channels of the Jamuna River was flowing through the Madargonj Upazila, which was shifted towards west during the last fifteen to twenty years of time. A few parts of that channel now-a-days became beel or pond used by the local people for fisheries and agriculture purposes. The morphological behaviour of the Jamuna River was not like a threat for further erosion in that area for last thirty years but now-a-days it became harmful as the rate of river bank erosion was increases time to time particularly in that area as described above. A trust of Water Resources ministry, the CEGIS had been made a report "Prediction of river erosion along the Jamuna, the Ganges and the Padma Rivers in 2015" described the prediction of severe river bank erosion at Balijuri & Pakerdaha area of Madargonj upazila of Jamalpur district and at Jamthal area of Sariakandi upazila of Bogra district. Practically, the river bank erosion was started in that area and if this type of erosion was going on, the entire area may fall in to a natural disastrous situation. The socio-economic condition of the people of that area may threatened by the loss of river bank erosion.

31.2 Justification/Adequacy

The issue of mitigation of river bank erosion can address by implementing permanent protective works along the left bank of the Jamuna River only. Regarding the issue, BWDB formulate a technical committee consisting of at least seven members of different discipline of BWDB head quarter and two external members from other institutions. The committee members visit the erosion prone area physically and also made few discussions with the people's representative of the locality. Finally, the technical committee submit a detail report with the recommendations to implement permanent protective works of length 6.25 kilometer which costs about 584.72 crore BDT. Accordingly, BWDB concern field office prepares the DPP of the proposed project and submit for the approval. Meanwhile, BWDB had been implemented this type of project addressing the river bank erosion issue in several parts of the country for at least last 35 to 40 years, which are appeared quite adequate to stop the river bank erosion for different big, medium and small rivers flowing through out the various regions of the Bangladesh. Therefore, this project may consider justified for addressing the problem arising from the Jamuna River left bank erosion issue.

31.3 Objectives

Main objectives of the project are:

- To arrest river bank erosion of approximately 2000 ha area by construction of River Bank Protection works for a length of 6.75 km.;
- To protect Balijuri and Pakerdah union of Jamalpur district and Jamthal area under Sariakandi Upazila of Bogura district from erosion of the Jamuna River and thereby save various government and non-government educational institutions, religious establishments, agricultural land, crops, houses, etc. costing approximately Tk. 231125.00 lakh;



- To improve the socio-economic condition of the project area and resist the adverse impact of the national economy;
- To reduce poverty and create opportunities for employment.

31.4 Project revision with reasons

The project was approved by the ECNEC on 10-04-2020 with a project implementation period from April 2020 to June 2023. But the physical work starts from July 2021. After starting the physical works, at the downstream of the project area, the river morphological changes occurred and a new area was affected by the bank erosion. Regarding the issue, project implementing authority submit a short report to the ministry of water resources. Ministry instruct the BWDB to form a technical committee to visit the newly developed erosion prone area at downstream of the project area and also to submit a detail report regarding the issue including their recommendation. Accordingly, the technical committee prepare a detail report after visiting the area with their recommendation. Therefore, project revision was needful to address the project vulnerability along with the new erosion prone area at downstream of the project area.

32. Rationale of the project (Consider the following issues):

32.1 Concept

The problem of river bank erosion in Bangladesh is a common phenomenon. Bangladesh is a delta of Ganges-Brahmaputra-Meghna, the three mighty rivers of the south-east Asia. This is a large transboundary river basin that significantly impacts Bangladesh. As the downstream riparian nation, Bangladesh is heavily reliant on and affected by the water resources and flows within the GBM basin, particularly from the Ganges, Brahmaputra, and Meghna rivers. Flooding is a major concern for Bangladesh due to its location at the basin's outlet, and the country utilizes flood forecasting systems to mitigate its effects. Along with the flooding, river bank erosion is the other significant problem arises during rainy season in various parts of the Bangladesh. The project concept was appropriate to protect the area against river bank erosion. It was an investment project where investment came from the grant of GoB. By investing the money estimated for the project, construction of permanent protective work along the left of bank of Jamuna River had been implemented. The protective works will stop the river bank erosion; the vulnerability of the area will fixed against river bank erosion. Therefore, socio-economic condition of the locality will improve considerably.

32.2 Design

The design of the physical work of the project was to construct protective works by placing and dumping C. C. blocks of various sizes and 250 kg sizes sand filled geo-bags. The design of protective works is conventional type. BWDB had been constructed permanent protective works all over the Bangladesh during last 30-35 years with no adverse effect. The implemented protective work's design was incorporated in the DPP of the project and after approval of the DPP, the design was reviewed accordingly as per the latest condition of the river morphology by the design circle-1 of BWDB design directorate. The works had been implemented as per the approved design, drawing and specifications of BWDB.

32.3 Location

To protect the locality i. e. Pakerdaha & Balijuri area of Madargonj upazila of Jamalpur district and Jamthal area of Sariakandi upazila of Bogra district from the Jamuna River bank erosion, this project proposal was prepared by BWDB submitted for approval by the competent authority. The concept of the project was perfectly rationale because permanent protective work constructed by placing and dumping of C. C. blocks and sand filled geo-bags, which is the most conventional measure to protection against river bank erosion, which is used for ages. The design of the protection works is also used for ages and there are no negative findings yet for this type of civil works implemented along the river bank in Bangladesh.

32.4 Timing

The project titled "Protection from the erosion of Jamuna River at Pakerdaha & Balijuri of Madargonj Upazila of Jamalpur district and at Jamthal of Sariakandi Upazila of Bogra district (1st Revised)" was approved in the ECNEC meeting held on 10 March, 2020. Implementation period as per the approved DPP was from March 2020 to June 2023. Due to the change of river morphology, the DPP of the project needs to revised and also the implementation period was extended for one year. Moreover, one year no cost time extension was required due to the scarcity of fund allocation. Therefore, finally the implementation period of the project was from March 2020 to June 2025. The project has been completed within the latest implementation period.


33. Brief description on planning and financing of the project and its applicability (Consider the following issues):

33.1 Project Identification

The Project is located at Pakerdaha and Balijuri area of Madargonj upazila of Jamalpur district and Jamthal area of Sariakandi Upazila of Bogra district. The project was conceived to protect the erosion prone area as mentioned above from the erosion of Jamuna River. The project was financed by the Govt of Bangladesh.

33.2 Project Preparation

Jamthal area of Kajla union of Sariakandi upazila of Bogra district and Pakerdah & Balijuri union of Madargonj upazila of Jamalpur district situated on the left bank of Jamuna River. The erosion of the left bank of the Jamuna River has emerged as a threat to the area. As the house-hold of the local people and important infra-structures of that area continue to be threatened by river erosion, a project has been formulated to implement permanent protective works in the area. Mr. Mirza Azam, the honorable the then state minister, ministry of Jute and textile, peoples republic of Bangladesh sent a demi-official letter to the honorable the then state minister, Ministry of Water Resources, peoples republic of Bangladesh, requesting to formulate and implement a development project in order to prevent the river bank erosion of the left bank of Jamuna River at Madargonj and Sariakandi upazila of Jamalpur and Bogra district respectively. BWDB had been formed a technical committee to recommend with detail report about the left bank erosion of Jamuna River at the above mentioned area. Based on the recommendation of the technical committee, BWDB, Jamalpur office had been prepared the DPP of the project consisting of the major physical component as mentioned below:



Physical Work	Location	Length	Estimated Cost (Lakh Tk.)
iii) Permanent Protective Work	Pakerdaha and Balijuri of Madargonj Upazila and Jamthal area of Sariakandi Upazila	6.75 Km.	49640.91
iv) End Termination	Do	2 Nos.	7568.09

33.3 Appraisal

As per the decision of the appraisal Committee meeting DPP was recast by the BWDB and sent to the Ministry of Planning for approval. The Project was approved by ECNEC on 10.03.2020.

33.4 Credit Negotiation

Not applicable

33.5 Credit Agreement

Not applicable

33.6 Credit Effectiveness

Not applicable

33.7 Loan Disbursement

Not applicable

33.8 Loan Conditions

Not applicable

33.9 Project Approval

The DPP of the project had been approved by ECNEC on 10 March, 2020 consisting of total project cost BDT 58424.72 Lakhs and project implementation period from April, 2020 to June, 2023. The DPP was revised based on the technical committee report including another 0.50 Km length of protective works at downstream of the existing length. The RDPP of the Project approved by the competent authority on 23.05.2023 with a cost of tk. 57441.00 lakh for implementation period April/2020 to June/2024. Thereafter, consequence Covid' 19 pandemic situation affect the budget allocation and implementation of the project. So the project implementation period was extended up to June 2025 without cost increases.

33.10 Others (specify): Nil.

34. Analysis of the post- implementation situation and result of the project (Consider following issues):

34.1 Whether the beneficiaries of the project have clear knowledge about the Target/Objectives of the project. Yes.

34.2 Programme for use of created-facilities of the project: The stakeholders and public are directly taking advantages of the created facilities of the project.

34.3 O & M Program of the project: Repair and maintenance of the implemented works (if necessary) will be done by the regular O & M allocation

34.4 Impact of the project (Direct & Indirect)

Direct

The project was conceived to protect the erosion affected area of Madargonj and Sariakandi upazila. By implementation of the permanent protective works the left bank erosion of that area been stopped and the river course has been shifted towards west. The implementation of the project has increased the safety of the general public in the project area against river erosion and the socio-economic condition also improved considerably. No adverse impact on this project.

Indirect

Improvement of overall economic, social & socio-economic condition

34.5 Transfer of Technology and Institutional Building through the project.

Not Applicable

34.6 Employment generation through the project.

Due to project interventions, areas where creation of notable amount of employment opportunities anticipated are:

Job opportunity in river bank protection

Job opportunity in boost up agriculture

Job opportunity in city extension works

Job opportunity in trade and commerce

Participatory process in implementation.

Employment generation for skilled and unskilled labour.

34.7 Possibility of Self-employment.

The project will provide significant employment opportunities due to creation of overall safety against river bank erosion. Factories and industries will be setup by the entrepreneur beside the river. People will be able to generate self-employment in their locality.

34.8 Possibility of Women-employment opportunity.

In the changed socio-economic situation women are compelled to migrate increasingly to urban areas in search of employment. Implementation of the project will directly create huge employment opportunity for rural women in protective works. Factories and industries will be setup along the river bank, many of the women will be able to have employment remaining in their locality and thereby avoiding the odds of living isolated from their family and the locality.

34.9 Women's participation in development.

Yes.

34.10 Probable Impact on Socio-Economic activity.

The most affected groups, being daily labors, will directly benefited from enhanced employment in construction works, other related works as well as expanding agricultural sector. As wage increase, consumption of daily food and other necessities by poor households will also increase. Implementation of project will directly create huge employment opportunity for rural man/women in protective works. Factories and industries will be setup along the river bank, many of the women will be able to have employment

remaining in their locality and thereby avoiding the odds of living isolated from their family and the locality. Hence, socio-economic balance in the locality has been achieved.

34.11 Impact on environment.

Environmental impact was assessed by technical committee during feasibility study and no adverse impact was identified by proposed interventions. The main objective of the project is, to protect river bank erosion by placing and dumping C.C. blocks and sand filled geo-bags in the project area. So, the project is environment friendly.

34.12 Sustainability of the project.

The project will be sustainable provided repair and maintenance of the implemented protective works, if necessary, will be executed on regular basis.

34.13 Contribution to poverty alleviation/reduction.

The project will directly increase agricultural production in the area. Thus the hard line poverty will be alleviated by virtue of both increase in income and employment. The most affected groups, being daily labourers, will directly benefited from enhanced employment in construction works, other related works as well as expanding agricultural sector. As wage increase, consumption of daily food and other necessities by poor households will also increase, thereby reducing the extent of poverty line in the project area

34.14 Opinion of the public representatives, local elite, local administration, teachers, religious leaders, women's representatives etc.

Positive remarks regarding the Project.

34.15 Contribution of Micro-credit programs and Comments on overlapping with any NGO activities.

Not Applicable.

35. Problems encountered during Implementation (with duration & steps taken to resolve those) (Consider following issues):

35.1 Project management: *Didn't arise*

35.2 Project Director: *Didn't arise*

35.3 Land Acquisition: *Not Applicable*

35.4 Procurement: *Didn't arise*

35.5 Consultancy: *Didn't arise*

35.6 Contractor: *Two Contractors failed to complete the works within the stipulated time.*

35.7 Manpower: *Didn't arise*

35.8 Law & Order: *Didn't arise*

35.9 Natural calamity: *Problem due to natural calamity was arisen from flood in the project area*

35.10 Project financing: *Didn't arise*

35.11 Allocation and release: *Scarcity of fund allocation arises during the corona pandemic.*

35.12 Design formulation/approval: *Didn't arise*

35.13 Project aid disbursement and re-imbursement: *Not applicable*

35.14 Mission of the development partners: *Not applicable*

JSK

- 35.15 Time & Cost Over-run: *Addition time was required to complete the project due to insufficient fund allocation.*
- 35.16 Project Monitoring: *Didn't arise*
- 35.17 Delay in Decision: *Didn't arise*
- 35.18 Transport, Training: *Not Applicable*
- 35.19 Approval and Others: *Didn't arise*

36. Remarks & Recommendations of the Project Director:


The project is a conventional investment project. The main objective of the project is to protect the erosion prone area named Pakerdah and Balijuri of Madargonj upazila and Jamthal area of Sariakandi upazila of Jamalpur and Bogra district respectively from the left bank erosion of Jamuna River. The main component of the project is 6.75 Km permanent protective works and two end termination at upstream and downstream of the protective works. After the approval of the project by ECNEC, the project was categorized as B-category by finance ministry. As a result, the project yearly allocation was not satisfactory as planned in the DPP. Again, Jamuna River morphology of the project area had been changed after starting the implementation of the project, which commit to made a revision of the project.

The physical works of the project had been implemented through institutional monitoring. The physical work's quality and quantity had been ensured as per the design and specifications by the project implementing officials of BWDB, Jamalpur. Also, the high officials of BWDB and MoWR had been visited the project sites regularly to ensure the quality of the physical works to be implemented. BWDB's central Task-force had been ensured the quality of C.C. blocks and geo-textile bags by laboratory testing and the quantity of those by physical counting at site.

After the implementation of the permanent protective works under this project, the physical safety and sense of security against Jamuna River erosion have been developed among the peoples of the locality and investment also have been increased in personal housing and commercial building construction which also have positive impacts on agriculture and fish resources production and land prices.

Furthermore, regular repair and maintenance of the protective works, if necessary, will increase the sustainability of the project.

Date.....20/10/2025.....




Signature and seal of the Project Director

(Md. Sirajul Islam)
Superintending Engineer
Tangail WD Circle
BWDB, Tangail

37. Remarks/Comments of Agency Head:

The main objective of the project was to protect river bank erosion permanently by implemented permanent protective works along the left bank of the Jamuna River at Madargonj and Sariakandi upazila of Jamalpur and Bogra district respectively. The total length of the protective works was 6.75 Km and two end termination, one at upstream and one at downstream of the protective work. After implementation of the protective works under this project, it is observed that the erosion of Jamuna River has been stopped at the project area. The livelihood and the private and public properties situated near the Jamuna River had been saved from the threat of river erosion by implementing the project. Therefore, for the sustainability of the protective works, regular monitoring should be strengthened to comply with the repair and maintenance works, if needed.

Date.....



08.11.2024

Signature and seal of Agency Head

(Md. Enayet Ullah)
ID No. 670705001
Director General
BWDB, Dhaka.

38. Remarks/Comments of the Secretary/Senior Secretary of the Ministry/Division:

The project has been completed within the implementation period successfully. Now a regular monitoring should be ensured by the concern office of the Bangladesh Water Development Board, for sustainability of the project's physical works, which will ensure the best outcome from the investment of the Government of Bangladesh.

Date.....

Signature and seal of Secretary

Annexure-1(a)

Information Related to Procurement of Goods:

As per Project Document		Estimated Cost. (Taka in Lac)	Procurement Method	Approving Authority	Date of Tender Invitation	Name of Newspaper	Date of Opening	Date of Approval	Date of NOA	Contract Price & Date	Actual Payment	Date of Completion	
Package No	Description of Package											As per Contract	Actual
Jeep-01/19-20	One Jeep manufactured by Progoti Ltd. with 5-doors and not beyond 2500 cc	(3) Plan 61.00	(4) DPM	(5) DG, BWDB	(6) 01/04/2023	(7)	(8)	(9)	(10) 30/06/2023	(11) 61.00	(12)	(13) 31/12/2023	(14) 31/12/2023
		Actual 61.00	DPM	DG, BWDB	01/04/2023	N/A	25/06/2023	30/06/2023	30/06/2023		61.00		
		Deviation: 0.00	-	-	-		-	-	-	-			
Computer-02/19-20	One Desktop computer with one laser printer and one scanner	Plan 0.80	RFQ	EE, BWDB	27/05/2021	N/A			08/06/2021	0.80	0.80	28/06/2021	28/06/2021
		Actual 0.80	RFQ	EE, BWDB	27/05/2021		06/06/2021	06/06/2021	08/06/2021				
		Deviation: 0.00	-	-	-		-	-	-	-			
Photocopier-03/19-20	Purchase of one photocopier	Plan 1.50	RFQ	EE, BWDB	27/05/2021	N/A			08/06/2021	1.50	1.50	28/06/2021	28/06/2021
		Actual 1.50	RFQ	EE, BWDB	27/05/2021		06/06/2021	06/06/2021	08/06/2021				
		Deviation: 0.00	-	-	-		-	-	-	-			
Furniture-04/19-20	Purchase of one set furniture for office	Plan 2.00	RFQ	EE, BWDB	15/05/2022	N/A			25/05/2022	2.00	2.00	29/06/2022	29/06/2022
		Actual 2.00	RFQ	EE, BWDB	15/05/2022		23/05/2022	23/05/2022	25/05/2022				
		Deviation: 0.00	-	-	-		-	-	-	-			
Computer-05/22-23	Two Desktop computer with laser printer and scanner	Plan 1.70	RFQ	EE, BWDB	22/11/2023	N/A			03/12/2023	1.70	1.70	26/02/2024	30/01/2024
		Actual 1.70	RFQ	EE, BWDB	22/11/2023		30/11/2023	30/11/2023	03/12/2023				
		Deviation: 0.00	-	-	-		-	-	-	-			

* Please mention Dates for plan and actual

* Deviation in days (difference between plan and actual)

* Plan as per procurement plan described in project document

Information Related to Procurement of Works:

As per Project Document Package No	Description of Package	Estimated Cost. (Taka in Lac)	Procurement Method	Approving Authority	Date of Tender Invitation	Name of Newspaper	Date of Opening	Date of Approval	Date of NOA	Contract Price & Date	Actual Payment	Date of Completion As per Contract	Date of Completion Actual
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)	(14)
BPW- Paker- 01/20-21	River bank protection work along the left bank of Jamuna River from km. 0.000 to km. 0.300 = 0.300 km at Jamthai in Upazila-Sariakandi of Bogura District during the year 2021-22 & 2022-23	Plan 2056.48 Actual 2056.48 Deviation	OTM	DG, BWDB	09/01/2022	The daily Somokal, The daily Financial Express	07/02/2022	03/04/2022	18/04/2022	2056.48	2051.10	27/06/2023	17/04/2023
BPW- Paker- 02/20-21	River bank protection work along the left bank of Jamuna River from km. 0.300 to km. 0.600 = 0.300 km at Pakerdaha in Upazila-Madaganj of Jamalpur district during the year 2021-22 to 2022-23	Plan 2469.31 Actual 2469.31 Deviation	OTM	DG, BWDB	09/01/2022	The daily Somokal, The daily Financial Express	07/02/2022	03/04/2022	18/04/2022	1958.11	1936.20	01/04/2025	01/04/2025
BPW- Paker- 03/20-21	River bank protection work along the left bank of Jamuna river from km. 0.600 to km. 0.900 = 0.300 km at Pakerdaha in Upazila-Madaganj of Jamalpur district during the year 2020-21 to 2022-23	Plan 2491.59 Actual 2491.59 Deviation	OTM	DG, BWDB	09/01/2022	The daily Somokal, The daily Financial Express	07/02/2022	03/04/2022	18/04/2022	1978.27	1947.34	01/04/2025	18/06/2025
BPW- Paker- 04/20-21	River bank protection work along the left bank of Jamuna river from km. 0.900 to km. 1.200 = 0.300 km at Jamthai in Upazila-Sariakandi of Bogura district during the year 2021-22 & 2022-23	Plan 2501.01 Actual 2501.01 Deviation	OTM	DG, BWDB	09/01/2022	The daily Somokal, The daily Financial Express	07/02/2022	03/04/2022	18/04/2022	2114.53	2094.45	15/03/2024	15/03/2024
End termination-US- 05/20-21	U/S End Termination along the left bank of Jamuna river from km. 0.000 to km. 0.200 = 0.200 km at Pakerdaha union in Upazila-Madaganj of Jamalpur District during the year 2021-22 & 2022-23.	Plan 2699.92 Actual 2699.92 Deviation	OTM	DG, BWDB	03/01/2022	The daily Somokal, The daily Financial Express	07/02/2022	03/04/2022	18/04/2022	2005.03	2004.25	20/06/2024	20/06/2024

B22

As per Project Document Package No	Description of Pack age	Estimated Cost. (Taka in Lac)	Procurement Method	Approving Authority	Date of Tender Invitation	Name of Newspaper	Date of Opening	Date of Approval	Date of NOA	Contract Price & Date	Actual Payment	Date of Completion	
												As per Contract	Actual
(1) End terminatio n-US- 06/20-21	(2) U/S End Termination along the left bank of Jamuna river from km.0.200 to km. 0.400 = 0.200 km at Pakardah union in Upazila - Madaganj of Jamalpur district during the year 2021-22 & 2022-23. e- Tender ID No-645000. Package No:	(3) Plan 2140.13	(4) OTM	(5) DG, BWDB	(6) 09/01/20 22	(7) The daily Somokal, The daily Financial Express	(8)	(9)	(10) 18/04/2022	(11) 1636.72	(12) 1623.81	(13) 31/05/2025	(14) 22/06/2025
		Actual 2140.13	OTM	DG, BWDB	09/01/20 22		07/02/20 22	03/04/2022	18/04/2022				
		Deviation	-		-				-				
End terminati on-US- 07/20-21	U/S End Termination along the left bank of Jamuna River from km.0.400 to km.0.52334 = 0.12334 km at Pakardah union in Upazila -Madaganj of Jamalpur district during the year 2021-22 & 2022- 23.	Plan 1184.52	OTM	CE, BWDB	09/01/20 22	The daily Somokal, The daily Financial Express			18/04/2022	910.05	849.74	31/05/2025	22/06/2025
		Actual 1184.52	OTM	CE, BWDB	09/01/20 22		07/02/20 22	03/04/2022	18/04/2022				
		Deviation	-		-				-				
BPW- Jamthal- 08/20-21	River bank protection work along the left bank of Jamuna River from km.1.200 to km.1.550 = 0.350km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2021-2022 & 2022- 2023.	Plan 2891.08	OTM	DG, BWDB	09/01/20 22	The daily Somokal, The daily Financial Express			18/04/2022	2325.42	2196.51	31/05/2025	22/06/2025
		Actual 2891.08	OTM	DG, BWDB	09/01/20 22		07/02/20 22	03/04/2022	18/04/2022				
		Deviation	-		-				-				
BPW- Jamthal- 09/20-21	River bank protection work along the left bank of Jamuna River from km.1.550 to km.1.900 = 0.350km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2021-2022 & 2022- 2023.	Plan 2891.12	OTM	DG, BWDB	09/01/20 22	The daily Somokal, The daily Financial Express			18/04/2022	2329.01	1978.86	31/05/2025	22/06/2025
		Actual 2891.12	OTM	DG, BWDB	09/01/20 22		07/02/20 22	03/04/2022	18/04/2022				
		Deviation	-		-				-				
BPW- Jamthal- 10/20-21	River bank protection work along the left bank of Jamuna river from km.1.900 to km.2.250 = 0.350 km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2020-2021 & 2021- 2022.	Plan 2770.14	OTM	DG, BWDB	11/10/20 20	The Daily Songbad, The Financial Express, The daily Ajker Jamalpur			09/01/2021	2160.37	2057.72	31/05/2025	22/06/2025
		Actual 2770.14	OTM	DG, BWDB	11/10/20 20		10/11/20 20	29/12/2020	09/01/2021				
		Deviation	-		-				-				

182

As per Project Document Package No	Description of Pack age	Estimated Cost. (Taka in Lac)	Procurement Method	Approving Authority	Date of Tender Invitation	Name of Newspaper	Date of Opening	Date of Approval	Date of NOA	Contract Price & Date	Actual Payment	Date of Completion	
												As per Contract	Actual
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)	(14)
BPW- Jamthal- 11/20- 21.	River bank protection work along the left bank of Jamuna river from km. 2.250 to km.2.600 = 0.350 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2757.51	OTM	DG, BWDB	11/10/20 20	The Daily Songbad, The Financial Express, The daily Ajker Jamaipur	10/11/20 20		09/01/2021	2540.46	2086.57	31/05/2025	25/05/2025
		Actual 2757.51	OTM	DG, BWDB	11/10/20 20			29/12/2020	09/01/2021				
		Deviation	-		-				-				
BPW- Jamthal- 12/20-21	River bank protection work along the left bank of Jamuna river from km. 2.600 to km.2.950 = 0.350 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2758.56	OTM	DG, BWDB	11/10/20 20	The Daily Songbad, The Financial Express, The daily Ajker Jamaipur			09/01/2021	2264.69	2252.36	31/05/2025	22/06/2025
		Actual 2758.56	OTM	DG, BWDB	11/10/20 20		10/11/20 20	29/12/2020	09/01/2021				
		Deviation	-		-				-				
BPW- Jamthal- 13/20- 21.	River bank protection work along the left bank of Jamuna river from km. 2.950 to km.3.300 = 0.350 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2737.18	OTM	DG, BWDB	11/10/20 20	The Daily Songbad, The Financial Express, The daily Ajker Jamaipur			09/01/2021	2171.45	2131.56	02/01/2024	02/01/2024
		Actual 2737.18	OTM	DG, BWDB	11/10/20 20		10/11/20 20	29/12/2020	09/01/2021				
		Deviation	-		-				-				
BPW- Jamthal- 14/20-21	River bank protection work along the left bank of Jamuna river from km. 3.300 to km. 3.650 = 0.350 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2731.96	OTM	DG, BWDB	11/10/20 20	The Daily Songbad, The Financial Express, The daily Ajker Jamaipur			09/01/2021	2167.75	2150.89	31/12/2023	31/03/2024
		Actual 2731.96	OTM	DG, BWDB	11/10/20 20		10/11/20 20	29/12/2020	09/01/2021				
		Deviation	-		-				-				
BPW- Jamthal- 15/20-21	River bank protection work along the left bank of Jamuna river from km. 3.650 to km.4.000 = 0.350 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2734.34	OTM	DG, BWDB	11/10/20 20	The Daily Songbad, The Financial Express, The daily Ajker Jamaipur			09/01/2021	2164.52	2137.59	02/01/2025	02/01/2025
		Actual 2734.34	OTM	DG, BWDB	11/10/20 20		10/11/20 20	29/12/2020	09/01/2021				
		Deviation	-		-				-				
BPW- Jamthal- 16/20-21	River bank protection work along the left bank of Jamuna river from km. 4.000 to km.4.350 = 0.350 km at Jamthal in Upazila- Sariakandi of Bogra district	Plan 2722.41	OTM	DG, BWDB	11/10/20 20	The Daily Songbad, The Financial Express, The			09/01/2021	2218.99	2212.21	14/03/2024	12/03/2024
		Actual 2722.41	OTM	DG, BWDB	11/10/20 20		10/11/20 20	29/12/2020	09/01/2021				

JSR

As per Project Document Package No	Description of Pack age	Estimated Cost. (Taka in Lac)	Procurement Method	Approving Authority	Date of Tender Invitation	Name of Newspaper	Date of Opening	Date of Approval	Date of NOA	Contract Price & Date	Actual Payment	Date of Completion	
												As per Contract	Actual
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)	(14)
	during the year 2020-21 & 2021-22.	Deviation	-		-	daily Ajker Jamalpur							
BPW- Jamthal- 17/20-21	River bank protection work along the left bank of Jamuna river from km. 4.350 to km.4.700 = 0.350 km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2727.05	OTM	DG, BWDB	11/10/20	The Daily Songbad, The Financial Express, The daily Ajker Jamalpur	10/11/20	29/12/2020	09/01/2021	2216.66	2188.67	14/03/2024	13/03/2024
		Actual 2727.05	OTM	DG, BWDB	11/10/20		20		09/01/2021				
		Deviation	-		-								
BPW- Jamthal- 18/20-21	River bank protection work along the left bank of Jamuna river from km. 4.700 to km.5.050 = 0.350 km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2732.29	OTM	DG, BWDB	11/10/20	The Daily Songbad, The Financial Express, The daily Ajker Jamalpur			09/01/2021	2221.34	2217.71	14/03/2024	10/03/2024
		Actual 2732.29	OTM	DG, BWDB	11/10/20		10/11/20	29/12/2020	09/01/2021				
		Deviation	-		-								
BPW- Jamthal- 19/20-21	River bank protection work along the left bank of Jamuna river from km. 5.050 to km.5.400 = 0.350 km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2804.21	OTM	DG, BWDB	11/10/20	The Daily Songbad, The Financial Express, The daily Ajker Jamalpur			09/01/2021	2512.76	2512.73	20/06/2023	19/06/2023
		Actual 2804.21	OTM	DG, BWDB	11/10/20		10/11/20	29/12/2020	09/01/2021				
		Deviation	-		-								
BPW- Jamthal- 20/20-21	River bank protection work along the left bank of Jamuna river from km. 5.400 to km.5.750 = 0.350 km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 2790.78	OTM	DG, BWDB	11/10/20	The Daily Songbad, The Financial Express, The daily Ajker Jamalpur			09/01/2021	2500.32	2497.61	20/06/2023	19/06/2023
		Actual 2790.78	OTM	DG, BWDB	11/10/20		10/11/20	29/12/2020	09/01/2021				
		Deviation	-		-								
BPW- Jamthal- 21/20-21	River bank protection work along the left bank of Jamuna River from km. 5.750 to km.6.000 = 0.250 km at Jamthal in Upazila-Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Plan 1962.10	OTM	ADG, BWDB	11/10/20	The Daily Songbad, The Financial Express, The daily Ajker Jamalpur			09/01/2021	1704.51	1699.93	12/12/2024	03/12/2024
		Actual 1962.10	OTM	ADG, BWDB	11/10/20		10/11/20	29/12/2020	09/01/2021				
		Deviation	-	ADG, BWDB	-								
	River bank protection work along the left bank of	Plan 1955.87	OTM	ADG, BWDB	11/10/20	The Daily Songbad, The			09/01/2021	1699.60	1696.66	12/12/2024	28/10/2024

JSZ

As per Project Document Package No	Description of Pack age	Estimated Cost. (Taka in Lac)	Procur ement Metho d	Approving Authority	Date of Tender Invitation	Name of Newspaper	Date of Opening	Date of Approval	Date of NOA	Contract Price & Date	Actual Payment	Date of Completion	
												As per Contract	Actual
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)	(14)
BPW- Jamthal- 22/20-21	Jamuna River from km. 6.000 to km.6.250 = 0.250 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2020-21 & 2021-22.	Actual 1955.87 Deviation	OTM	ADG, BWDB	11/10/20 20	Financial Express, The daily Ajker Jamalpur	10/11/20 20	29/12/2020	09/01/2021				
			-		-				-				
End terminati on-DS- 23/22-23	D/S End Termination along the left bank of Jamuna river from km. 0.000 to km. 0.128 = 0.128 km at Jamthal area in Upazila- Sariakandi of Bogura District during the year 2022-23 & 2023-24.	Plan 1543.69 Actual 1543.38 Deviation	OTM	CE, BWDB	27/07/20 23	The Daily Pratidener Sangbad, The New Nation, Jamalpur Sangbad	28/08/20 23	10/09/2023	14/09/2023	1432.56	1432.06	31/05/2025	28/04/2025
			-	-	-				-				
				OTM	ADG, BWDB	27/07/20 23	The Daily Pratidener Sangbad, The New Nation, Jamalpur Sangbad	28/08/20 23	10/09/2023	14/09/2023	1792.52	1784.18	31/05/2025
BPW- Jamthal- 24/22-23	River bank protection work along the left bank of Jamuna River from km. 6.250 to km.6.500 = 0.250 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2022-23 & 2023-24.	Plan 1939.45 Actual 1939.17 Deviation	OTM	ADG, BWDB	27/07/20 23	The Daily Pratidener Sangbad, The New Nation, Jamalpur Sangbad	28/08/20 23	10/09/2023	14/09/2023				
			-		-				-				
				OTM	ADG, BWDB	27/07/20 23	The Daily Pratidener Sangbad, The New Nation, Jamalpur Sangbad	28/08/20 23	10/09/2023	14/09/2023			
BPW- Jamthal- 25/22- 23.	River bank protection work along the left bank of Jamuna River from km. 6.500 to km.6.750 = 0.250 km at Jamthal in Upazila- Sariakandi of Bogra district during the year 2022-23 & 2023-24.	Plan 1944.93 Actual 1944.65 Deviation	OTM	ADG, BWDB	27/07/20 23	The Daily Pratidener Sangbad, The New Nation, Jamalpur Sangbad	28/08/20 23	10/09/2023	14/09/2023	1750.19	1750.04	31/05/2025	28/05/2025
			-		-				-				
				OTM	ADG, BWDB	27/07/20 23	The Daily Pratidener Sangbad, The New Nation, Jamalpur Sangbad	28/08/20 23	10/09/2023	14/09/2023			

* Please mention Dates for plan and actual

* Deviation in days (difference between plan and actual)

* Plan as per procurement plan described in project document

Information Related to Procurement of Services:

As per Project Document	Package No	Description of Package	Estimated Cost. (Taka in Lac)	Procurement Method	Approving Authority	Date of Tender Invitation	Name of Newspaper	Date of Opening	Date of Approval	Date of LOA	Contract Price & Date	Actual Payment	Date of Completion	
													As per Contract	Actual
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)	(12)	(13)	(14)	
		Plan												
		Actual												
		Deviation												
		Actual												
		Deviation												
N/A														

* Please mention Dates for plan and actual

* Deviation in days (difference between plan and actual)


* Plan as per procurement plan described in project document

J Etc



গণপ্রজাতন্ত্রী বাংলাদেশ সরকার
পানিসম্পদ মন্ত্রণালয়

“জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি
উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙন হতে রক্ষা” শীর্ষক প্রকল্পের মধ্যবর্তী মূল্যায়ন
প্রতিবেদন

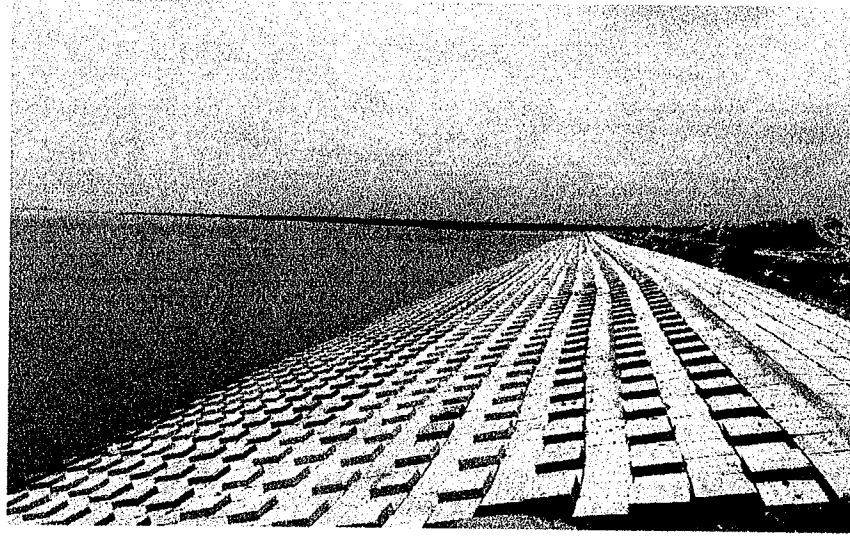

জানুয়ারি, ২০২৩

সূচিপত্র

ক্রমিক নং	বিষয়	পৃষ্ঠা
১.	প্রথম অধ্যায়ঃ প্রকল্পের বিবরণ	
১.১	প্রকল্পের পটভূমি	০১
১.২	প্রকল্প সংক্রান্ত সাধারণ তথ্যাবলি	০৪
১.৩	প্রকল্পের উদ্দেশ্য	০৪
১.৪	প্রকল্পের প্রধান প্রধান কার্যক্রম	০৪
১.৫	প্রকল্পের অঙ্গসমূহের ক্রমপুঞ্জীভূত বাস্তব ও আর্থিক অগ্রগতি (২০ নভেম্বর, ২০২২)	০৫
১.৬	প্রকল্পের মূল কাজের অগ্রগতির বিবরণ	০৬
১.৭	অনুমোদিত আরডিপিপি অনুসারে বছর ভিত্তিক বরাদ্দ ও প্রকৃত ব্যয়	০৬
১.৮	প্রকল্প পরিচালক সম্পর্কিত তথ্যাদি	০৬
২.	দ্বিতীয় অধ্যায়ঃ মধ্যবর্তী মূল্যায়ন	
২.১	মধ্যবর্তী মূল্যায়নের পটভূমি	০৭
২.২	মধ্যবর্তী মূল্যায়নের উদ্দেশ্য	০৭
২.৩	কমিটির গঠন ও কার্যপরিধি	০৭
২.৪	মূল্যায়ন পদ্ধতি	০৮
২.৫	মূল্যায়নের সীমাবদ্ধতা	০৯
৩.	তৃতীয় অধ্যায়ঃ প্রকল্প এলাকা পরিদর্শন	
৩.১	ভূমিকা	১০
৩.২	প্রকল্প এলাকা পরিদর্শনের বিবরণ	১০
৪.	চতুর্থ অধ্যায়ঃ জনপ্রতিনিধি, প্রকল্প সংশ্লিষ্ট কর্মকর্তা ও সুফলভোগীদের মতামত	
৪.১	জনপ্রতিনিধিদের মতামত	১৪
৪.২	প্রকল্প সংশ্লিষ্ট কর্মকর্তাদের মতামত	১৪
৪.৩	সুফলভোগীদের মতামত	১৪
৫.	পঞ্চম অধ্যায়ঃ কমিটির পর্যবেক্ষণ ও সুপারিশ	
৫.১	কমিটির পর্যবেক্ষণ	১৬
৫.২	কমিটির সুপারিশ	১৮

প্রথম অধ্যায়


প্রকল্পের বিবরণ

১.১। প্রকল্পের পটভূমি:

বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন কাজলা ইউনিয়ন এবং জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি ইউনিয়ন যমুনা নদীর বামতীরে অবস্থিত। জামালপুর জেলা বাংলাদেশের দরিদ্র জেলাগুলোর অন্যতম এবং এ কারণে গণপ্রজাতন্ত্রী বাংলাদেশ সরকার এ জেলায় বিভিন্ন উন্নয়নমূলক প্রকল্প গ্রহণ করেছে, যাতে এখানে বসবাসকারী জনগণের দ্রুত আর্থ-সামাজিক উন্নয়ন ঘটে। আলোচ্য অংশের বিগত কয়েক বছরের গুণল ম্যাপ পর্যালোচনায় দেখা গিয়েছে, সারিয়াকান্দি উপজেলার জামথল এলাকায় মারাত্মক নদী ভাঙ্গন রয়েছে এবং বামতীর ক্রমেই পূর্ব দিকে সরে যাচ্ছে। অন্যদিকে, নদীবক্ষে কয়েকটি চরের সৃষ্টি হয়েছে এবং চরগুলোর পরিধি ক্রমেই বৃদ্ধি পাচ্ছে। চর সৃষ্টি ও এর পরিধি বৃদ্ধি পাওয়া এবং যমুনা নদীর প্রবাহ তীর্থকভাবে বামতীর বরাবর আঘাত হানার কারণেই আলোচ্য অংশে নদীভাঙ্গনের তীব্রতা অত্যধিক বৃদ্ধি পেয়েছে। কাজলা ইউনিয়নের জামথল নামক স্থানসহ এর উজান ও ভাটিতে যমুনা নদীর বামতীরে বিগত কয়েক বছর যাবত মারাত্মক ভাঙ্গন অব্যাহত আছে।

গণপ্রজাতন্ত্রী বাংলাদেশ সরকারের বঙ্গ ও পাট মন্ত্রণালয়ের দায়িত্বে নিয়োজিত তদানীন্তন মাননীয় প্রতিমন্ত্রী, জনাব মির্জা আজম পানি সম্পদ মন্ত্রণালয়ের দায়িত্বে নিয়োজিত মাননীয় মন্ত্রী বরাবর আলোচ্য ভাঙ্গন বন্ধ করার কার্যকরী ব্যবস্থা নেওয়ার লক্ষ্যে অনানুষ্ঠানিক পত্র প্রদান করেন। উল্লেখ্য, নদীতীর হতে ২ কিঃমিঃ এর মধ্যে ২০০ মেগাওয়াটের একটি সোলার পাওয়ার প্লান্ট, পাট গবেষণা উপকেন্দ্র ও জুট টেক্সটাইল কমপ্লেক্স নির্মাণাধীন রয়েছে। তাছাড়া, মাদারগঞ্জ উপজেলা শহর এবং নদীতীরের মধ্যবর্তী অংশে বেশ কয়েকটি খাল ও নীচু খাঁড়ি আকৃতির ভূমিতল রয়েছে। ২০০ মেঃওয়াট সোলার পাওয়ার প্লান্টটি উল্লিখিত নীচু স্থান ভরাট করে বাস্তবায়ন করা হচ্ছে। এমতাবস্থায়, যমুনা নদীর বামতীরের অব্যাহত ভাঙ্গন বন্ধ করা না গেলে নির্মাণাধীন সোলার পাওয়ার প্লান্ট এবং পাট গবেষণা উপকেন্দ্র নদীভাঙ্গনের কবলে পড়বে। এতে জাতীয় অর্থনীতির উপর এক নেতিবাচক প্রভাব পড়ার আশঙ্কা রয়েছে। উপরন্তু, নীচু স্থান দিয়ে কালক্রমে নদীর স্রোতধারা সৃষ্টি হলে মাদারগঞ্জ উপজেলা বিস্তীর্ণ এলাকাসহ ভাটিতে অবস্থিত সরিয়াবাড়ী উপজেলার ব্যাপক এলাকা নদীভাঙ্গনের কবলে পড়বে। এ সমস্যার সমাধানকল্পে প্রকল্পটি গ্রহণ করা হয়।

(Handwritten signatures and marks)

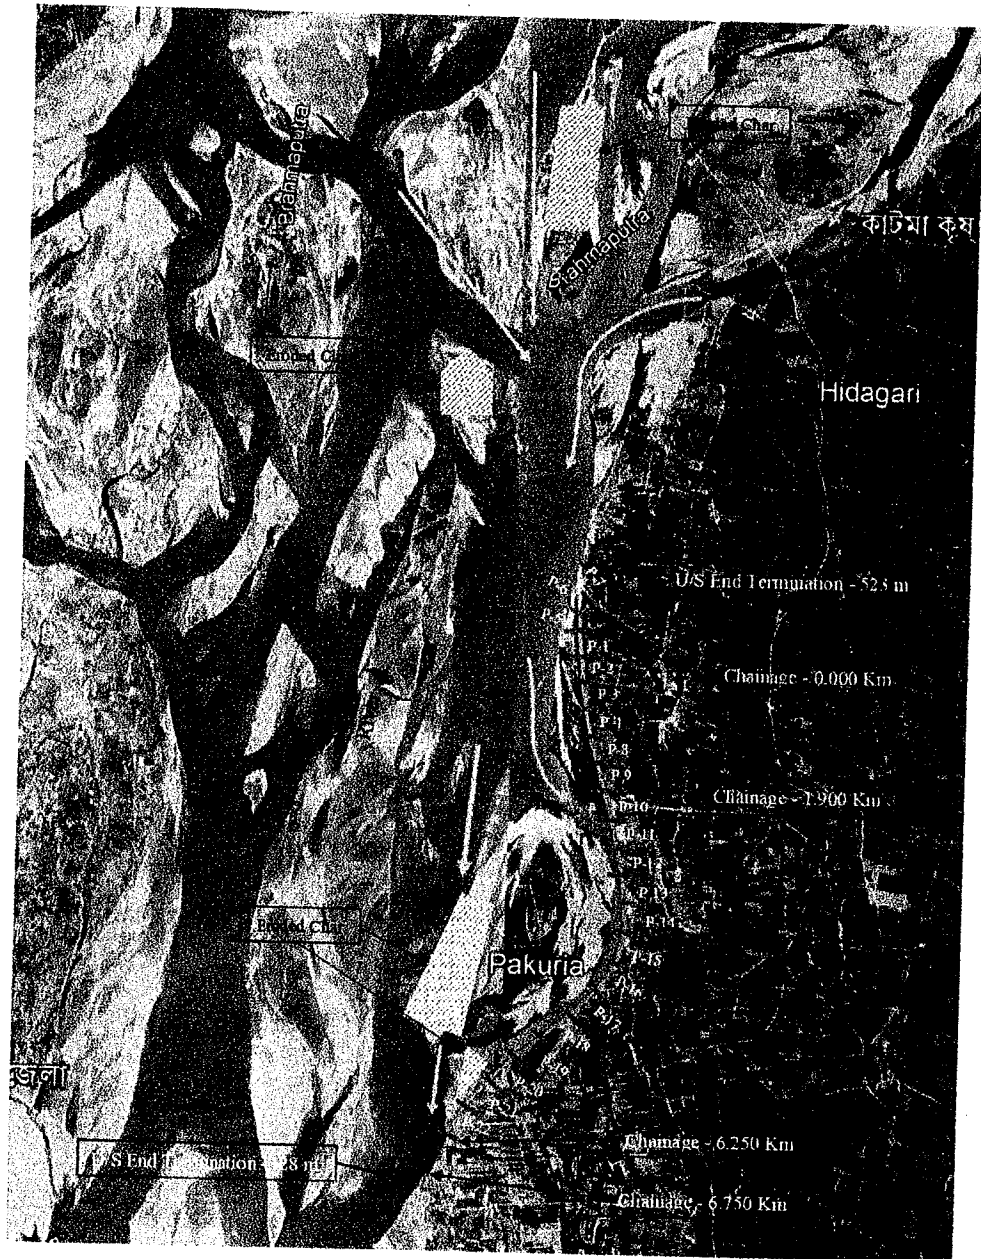

LEGENDS	
Flow Direction -	
Ongoing Protective Work -	
Proposed Protective Work -	
Eroded Char -	

প্রকল্প এলাকার অবস্থান (গুগল ম্যাপ)

Handwritten signatures and initials at the bottom of the page.

১.২। প্রকল্প সংক্রান্ত সাধারণ তথ্যাবলি:

(ক)	প্রকল্পের নাম	:	জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামথল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প।
(খ)	বাস্তবায়নকারী সংস্থা	:	বাংলাদেশ পানি উন্নয়ন বোর্ড।
(গ)	উদ্যোগী মন্ত্রণালয়	:	পানি সম্পদ মন্ত্রণালয়।
(ঘ)	প্রকল্প এলাকা	:	বিভাগ জেলা উপজেলা ময়মনসিংহ জামালপুর ও মাদারগঞ্জ ও সারিয়াকান্দি বগুড়া
(ঙ)	বাস্তবায়নকাল	:	এপ্রিল, ২০২০ খ্রিঃ হতে জুন ২০২৩ খ্রিঃ
(চ)	প্রকল্প ব্যয়	:	৫৮৪৭২.২৪ লক্ষ টাকা
(ছ)	প্রকল্পের ক্রমপুঞ্জীভূত অগ্রগতি (২০ নভেম্বর, ২০২২ পর্যন্ত)	:	আর্থিক অগ্রগতিঃ ১০৯৭১.৬৭ লক্ষ টাকা (১৮.৭৬%) বাস্তব অগ্রগতি (সার্বিক): ৪৬.১৮%।
(জ)	এডিপি/আরএডিপি বরাদ্দ	:	২০২২-২৩ অর্থবছরের এডিপি বরাদ্দ ১৫০০০.০০ লক্ষ টাকা।

১.৩। প্রকল্পের উদ্দেশ্য:

- (১) ৬.২৫০ কিঃমিঃ নদী তীর সংরক্ষণ কাজ বাস্তবায়ন করা হলে প্রকল্প এলাকার প্রায় ২০০০ হেক্টর ফসলী জমি নদী ভাঙ্গন হতে রক্ষা পাবে।
- (২) জামালপুর জেলার বালিজুরি ও পাকেরদহ ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলার জামথল এলাকা যমুনা নদীর ভাঙ্গনমুক্ত করাসহ বিভিন্ন সরকারী ও বেসরকারী অবকাঠামো, শিক্ষা ও ধর্মীয় প্রতিষ্ঠান, কৃষি-অকৃষিজমি, ফসলাদি, জনসাধারণের ঘরবাড়ী ইত্যাদি রক্ষা করা যার আনুমানিকমূল্য প্রায় ২৩১১২৫.০০ লক্ষ টাকা।
- (৩) আর্থ সামাজিক অবস্থার উন্নয়ন সহ এলাকার নিরাপত্তা ও জাতীয় অর্থনৈতিক বিরূপ প্রভাব রহিত করা।
- (৪) দারিদ্র বিমোচন ও কর্মসংস্থানের সুযোগ সৃষ্টি করা।

১.৪। প্রকল্পের প্রধান প্রধান কার্যক্রম:

ক্রঃ নং	ইকনমিক সাব-কোড অনুযায়ী বিভিন্ন অংশের (Items) বিবরণ	একক	পরিমাণ	ব্যয় (লক্ষ টাকায়)
	নির্মাণ ও পূর্তঃ			
১।	জামালপুর জেলার মাদারগঞ্জ উপজেলার বালিজুরি ও পাকেরদহ ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলার জামথল নামকস্থানে যমুনা নদীর বামতীরে সংরক্ষণ কাজ (কিঃমিঃ ০.০০ হতে কিঃমিঃ ৬.২৫০)	কিঃমিঃ	৬.২৫ কিঃমিঃ	৫০৭২৪.১৭
২।	জামালপুর জেলার মাদারগঞ্জ উপজেলার বালিজুরি ও পাকেরদহ ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলার জামথল নামকস্থানে যমুনা নদীর বামতীরে উজানে কিঃমিঃ ০.০০-তে ৫২৩.৩৪ মিটার দৈর্ঘ্যের ও ভাটিতে কিঃমিঃ ৬.২৫০-তে ১২৮ মিটার দৈর্ঘ্যের End Termination নির্মাণ।	সংখ্যা	২ টি	৭৫০৮.৭৭

১.৫। প্রকল্পের অঙ্গসমূহের ক্রমপুঞ্জিত বাস্তব ও আর্থিক অগ্রগতি:

(লক্ষ টাকায়)

আর্থিক কোড	ডিসিপি অনুযায়ী অংশের বিবরণ	ডিসিপি অনুযায়ী বরাদ্দ		ক্রমপুঞ্জিত অগ্রগতি (২০ নভেম্বর, ২০২২ পর্যন্ত)	
		ভৌত	আর্থিক	ভৌত (%)	আর্থিক
(ক) রাজস্ব ব্যয়ঃ সরবরাহ ও সেবা					
৩২৪১১০১	ভ্রমণ ব্যয়	১ দফা	২.০০	৭২.৫০%	১.৪৫
৩২৪৩১০১	পেট্রোল ও লুব্রিক্যান্ট	১ দফা	৫.০০	৯৬.০০%	৪.৮০
৩২৫৫১০২	প্রিন্টিং ও পাবলিকেশন	১ দফা	২.০০	৭৫.০০%	১.৫০
৩২৫৫১০৫	ষ্টেশনারী, সীল ও স্ট্যাম্প	১ দফা	২.০০	৭৫.০০%	১.৫০
৩২৫৫১০১	কম্পিউটার এন্ড ফটোকপি মেশিনের কনজিউমিবলস্	১ দফা	২.০০	৫০.০০%	১.০০
৩২৫৭১০৪	সার্ভে (ব্যথিমেন্ট্রিক ও ব্যাংক লাইন)	১ দফা	৫.০০	৮০.০০%	৪.০০
৩১১১৩৩২	মিড টার্ম ইভ্যালুয়েশান	১ দফা	১০.০০	০.৮৫%	০.০৮৫
৩১১১৩৩২	পিএসসি, পিআইসি ও টিইসি সদস্যগণের সম্মানী	১ দফা	৫.০০	৭৯.৮০%	৩.৯৯
৩২৫৮১০১	মোটর যানবাহন (বিদ্যমান ৪টি জিপ ও ৬টি মটর সাইকেলের মেরামত ও সংরক্ষণ)	১ দফা	৩.০০	৮৩.০০%	২.৪৯
৩২৫৮১০৩	কম্পিউটার ও অফিস সরঞ্জাম মেরামত	১ দফা	২.০০	৭৪.৫০%	১.৪৯
	সরবরাহ ও সেবা উপ-মোট (ক)		৩৮.০০	-	২২.৩০
(খ) মূলধন ব্যয়ঃ					
সম্পদ আহরণঃ					
৪১১২১০১	জামালপুর পওর বিভাগের জন্য প্রগতির তৈরি জিপ গাড়ী (২৫০০ সিঁসি'র উর্ধ্বে নয় ৫-দরজা) সংগ্রহ	১ সেট	৯৫.০০	১ টি	৬১.০০
৪১১২৩১০	ফটোকপিয়ার ক্রয়		১.৫০	১ টি	১.৫০
৪১১২২০২	কম্পিউটার ক্রয় (প্রিন্টার ও স্ক্যানার সহ)		০.৮০	১ টি	০.৮০
৪১১২৩১৪	অফিস ফার্নিচার ক্রয়		২.০০	১ দফা	২.০০
৪১১৩১০২	বৃক্ষ শস্য উদ্ভিজ্জ আবর্তক পন্য (বনায়ন)		২.০০	-	-
নির্মাণ কাজঃ					
৪১১১৩২১	জামালপুর জেলার মাদারগঞ্জ উপজেলার বালিজুরি ও পাকেরদহ ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলার জামখল নামকস্থানে যমুনা নদীর বামতীরে সংরক্ষণ কাজ (কিঃমিঃ ০.০০ হতে কিঃমিঃ ৬.২৫০)	৬.২৫ কিঃমিঃ	৫০৭২৪.১৭	৬.২৫ কিঃমিঃ (৫৩.২৩%)	১০৮৮৪.০৭
৪১১১৩২১	জামালপুর জেলার মাদারগঞ্জ উপজেলার বালিজুরি ও পাকেরদহ ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলার জামখল নামকস্থানে যমুনা নদীর বামতীরে উজানে কিঃমিঃ ০.০০-তে ৫২৩.৩৪ মিটার দৈর্ঘ্যের ও ভাটিতে কিঃমিঃ ৬.২৫০-তে ১২৮ মিটার দৈর্ঘ্যের End Termination নির্মাণ।	২ টি	৭৫০৮.৭৭	১ টি (আংশিক)	-
	খ) উপ-মোট (মূলধন):		৫৮৩৩৪.২৪	-	১০৯৪৯.৩৭
	গ) ফিজিক্যাল কন্ট্রিজেসি	১ দফা	৫০.০০	-	-
	ঘ) প্রাইস কন্ট্রিজেসি	১ দফা	৫০.০০	-	-
	সর্বমোট (ক+খ+গ+ঘ) :		৫৮৪৭২.২৪	৪৬.১৮%	১০৯৭১.৬৭ (১৮.৭৬%)

Handwritten signatures and marks at the bottom of the page, including a large '40' and various initials.

১.৬। প্রকল্পের মূল কাজের অগ্রগতির বিবরণ:

উন্মুক্ত দরপত্র পদ্ধতিতে দরপত্র আহবান করে কাজ বাস্তবায়ন করা হচ্ছে। ভৌত কাজের ২৩টি প্যাকেজের মধ্যে ২২টি প্যাকেজের কাজ চলমান রয়েছে। প্রকল্পের ডিপিপি সংশোধনের পরে অবশিষ্ট ১টি প্যাকেজের কাজের দরপত্র আহবান করা হবে। জুন, ২০২৩ এর মধ্যে কাজগুলি সমাপ্তির জন্য নির্ধারিত রয়েছে।

১.৬.১। নদী তীর সংরক্ষণ কাজঃ প্রকল্পের আওতায় মোট ৬.২৫০ কিঃমিঃ তীর সংরক্ষণ কাজ রয়েছে। ৬.২৫০ কিঃমিঃ তীর সংরক্ষণ কাজ চলমান রয়েছে যা জুন, ২০২৩ এর মধ্যে শেষ করার লক্ষ্যমাত্রা নির্ধারণ করা হয়েছে।

১.৬.২। এন্ড টার্মিনেশন নির্মাণ কাজঃ প্রকল্পের আওতায় মোট ২ টি এন্ড টার্মিনেশন কাজ রয়েছে। ৩টি প্যাকেজে উজানের ১ টি এন্ড টার্মিনেশন নির্মাণ এর কাজ চলমান রয়েছে যা জুন, ২০২৩ এর মধ্যে শেষ করার লক্ষ্যমাত্রা নির্ধারণ করা হয়েছে।

১.৭। অনুমোদিত ডিপিপি অনুসারে বহরভিত্তিক বরাদ্দ ও প্রকৃত ব্যয় (লক্ষ টাকা):

(লক্ষ টাকায়)

অর্থ বছর	ডিপিপি অনুযায়ী	প্রাপ্ত বরাদ্দ	প্রকৃত ব্যয়
২০১৯-২০	১০২.১০	-	-
২০২০-২১	১৪২৬৫.৩০	১৮০০.০০	১৭০৪.০৪
২০২১-২২	৩০৪৪০.৫২	৬৫০০.০০	৬৪৫৫.৬১
২০২২-২৩	১৩৬৬৪.৩২	১৫০০০.০০	২৮১২.০২ (২০ নভেম্বর, ২০২২ পর্যন্ত)
ক্রমপুঞ্জীভূত	৫৮৪৭২.২৪	২৩৩০০.০০	১০৯৭১.৬৭ (২০ নভেম্বর, ২০২২ পর্যন্ত)

১.৮। প্রকল্প পরিচালক সম্পর্কিত তথ্যাদিঃ

ক্রঃ নং	প্রকল্প পরিচালকের নাম	পদবী	কার্যকাল	
			হতে	পর্যন্ত
১।	মোঃ শাহজাহান সিরাজ	তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক	১৬/০৯/২০২০	১১/১০/২০২১
২।	মোঃ মাহফুজুর রহমান	তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক	১১/১০/২০২১	২৭/০৬/২০২২
৩।	মুহাম্মদ সিরাজুল ইসলাম	তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক	২৭/০৬/২০২২	বর্তমান সময় পর্যন্ত

Handwritten signatures and initials are present below the table, including a large signature on the left and several smaller ones on the right.

দ্বিতীয় অধ্যায়

মধ্যবর্তী মূল্যায়ন

২.১। মধ্যবর্তী মূল্যায়নের পটভূমি:

পানি সম্পদ মন্ত্রণালয়ের আওতায় বাংলাদেশ পানি উন্নয়ন বোর্ড কর্তৃক বাস্তবায়নাধীন “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামথল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প” শীর্ষক প্রকল্পটি ৫৮৪৭২.২৪ লক্ষ টাকা ব্যয়ে (সম্পূর্ণ জিওবি) এপ্রিল, ২০২০ হতে জুন, ২০২৩ মেয়াদে বাস্তবায়নের জন্য গত ১০/০৩/২০২০ খ্রিঃ তারিখে অনুষ্ঠিত একনেক সভায় অনুমোদিত হয়েছে। প্রকল্পের অনুমোদিত ডিপিপিতে পানি সম্পদ মন্ত্রণালয়, পরিকল্পনা কমিশন, আইএমইডি ও বাপাউবো’র প্রতিনিধিদের সমন্বয়ে মধ্যবর্তী মূল্যায়নের সংস্থান রয়েছে। প্রকল্প বাস্তবায়নকালের মাঝামাঝি সময়ে প্রকল্পের লক্ষ্য ও উদ্দেশ্যসমূহ অর্জনে অগ্রগতি বিশ্লেষণের মাধ্যমে নির্ধারণ করা এবং প্রকল্পের আউটপুট আরো কার্যকরভাবে স্থানীয় সুবিধাভোগীদের নিকট পৌঁছাতে কি ধরনের ব্যবস্থা গ্রহণ করা যায়, তার সুপারিশ প্রণয়নের লক্ষ্যে মধ্যবর্তী মূল্যায়ন শীর্ষক একটি কমিটি কার্য-পরিধিসহ প্রকল্পের ডিপিপিতে অন্তর্ভুক্ত করা হয়। মাঠ পর্যায়ে প্রকল্পের বাস্তবায়ন অগ্রগতি পর্যবেক্ষণের নিমিত্ত মূল্যায়ন কমিটির সদস্যগণ কর্তৃক গত ২৫-২৬ নভেম্বর, ২০২২ খ্রিঃ তারিখে সরেজমিনে প্রকল্প এলাকা পরিদর্শন করা হয়েছে।

২.২। মধ্যবর্তী মূল্যায়নের উদ্দেশ্য:

প্রকল্পের মধ্যবর্তী মূল্যায়নের মূল উদ্দেশ্য হলো প্রকল্পের অনুমোদিত প্রস্তাবনা অনুযায়ী সকল কাজ সম্পন্ন করা হয়েছে কিনা তা যাচাই করা এবং কাজের প্রয়োজনে সৃষ্ট যে কোন ধরনের পরিবর্তন উপস্থাপন করা। অন্য উদ্দেশ্যগুলো হল প্রকল্প বাস্তবায়নের মাধ্যমে উপকৃত সুফলভোগীদের সাথে আলোচনা করা এবং মাঠ পর্যায়ে প্রকল্প বাস্তবায়নের বিভিন্ন সমস্যা চিহ্নিত করা। অনুমোদিত ডিপিপি অনুযায়ী প্রকল্পের বাস্তব অগ্রগতি ৪০%-৪৫% অর্জন করার পর প্রকল্পের মধ্যবর্তী মূল্যায়ন কার্যক্রম পরিচালিত হবে। সংশ্লিষ্ট প্রকল্প পরিচালক প্রকল্পের অগ্রগতি নিশ্চিত করবেন ও মূল্যায়ন কমিটিকে মূল্যায়ন কার্যক্রম এগিয়ে নিতে সাহায্য করবেন।

২.৩। কমিটির গঠন ও কার্যপরিধি :

প্রকল্পের মধ্যবর্তী মূল্যায়ন কমিটি পরিকল্পনা কমিশন, আইএমইডি, পানি সম্পদ মন্ত্রণালয় এবং বাংলাদেশ পানি উন্নয়ন বোর্ড এর প্রতিনিধি দ্বারা গঠিত হবে। মধ্যবর্তী মূল্যায়নের লক্ষ্যে ডিপিপি’র সংস্থান অনুযায়ী পানি সম্পদ মন্ত্রণালয়ের পরিকল্পনা শাখা-২ এর স্মারক নং- ৪২.০০.০০০০.০৪০.০১৪.০০১.২০১৮-৩৩৩ তারিখ ২১/১১/২০২২ খ্রি: মোতাবেক নিয়োক্তভাবে একটি মধ্যবর্তী মূল্যায়ন কমিটি গঠন করা হয় :

ক্র:নং:	কমিটির সদস্য/প্রতিনিধি	কমিটিতে অবস্থান
০১.	অতিরিক্ত সচিব (পরিকল্পনা)/মুখ্যপ্রধান, পানি সম্পদ মন্ত্রণালয়	আহবায়ক
০২.	মুখ্য প্রধান, পরিকল্পনা কমিশনের সেচ উইং	সহ-আহবায়ক
০৩.	প্রতিনিধি, সংশ্লিষ্ট সেক্টর, আইএমইডি	সদস্য
০৪.	মুখ্যসচিব (উন্নয়ন-২ অধিশাখা), পানি সম্পদ মন্ত্রণালয়	সদস্য
০৫.	উপ প্রধান (সংশ্লিষ্ট), পানি সম্পদ মন্ত্রণালয়	সদস্য
০৬.	উপ প্রধান (সেচ উইং), পরিকল্পনা কমিশন	সদস্য

৭

২

৩

৪

৫

৬

৭

৮

৯

১০

১১

১২

১৩

১৪

১৫

১৬

১৭

১৮

১৯

২০

২১

২২

২৩

২৪

২৫

২৬

২৭

২৮

২৯

৩০

৩১

৩২

৩৩

৩৪

৩৫

৩৬

৩৭

৩৮

৩৯

৪০

৪১

৪২

৪৩

৪৪

৪৫

৪৬

৪৭

৪৮

৪৯

৫০

৫১

৫২

৫৩

৫৪

৫৫

৫৬

৫৭

৫৮

৫৯

৬০

৬১

৬২

৬৩

৬৪

৬৫

৬৬

৬৭

৬৮

৬৯

৭০

৭১

৭২

৭৩

৭৪

৭৫

৭৬

৭৭

৭৮

৭৯

৮০

৮১

৮২

৮৩

৮৪

৮৫

৮৬

৮৭

৮৮

৮৯

৯০

৯১

৯২

৯৩

৯৪

৯৫

৯৬

৯৭

৯৮

৯৯

১০০

ক্র:নং:	কমিটির সদস্য/প্রতিনিধি	কমিটিতে অবস্থান
০৭.	প্রতিনিধি, প্রধান পরিকল্পনা/প্রধান মনিটরিং, বাপাউবো, ঢাকা	সদস্য
০৮.	উপসচিব (উন্নয়ন শাখা-৩), পানি সম্পদ মন্ত্রণালয়	সদস্য
০৯.	প্রকল্প পরিচালক, “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামথল এলাকা যমুনা নদীর ভাষান হতে রক্ষা” শীর্ষক প্রকল্প	সদস্য
১০.	নির্বাহী প্রকৌশলী, জামালপুর পওর বিভাগ, বাংলাদেশ পানি উন্নয়ন বোর্ড, জামালপুর।	সদস্য
১১.	প্রতিনিধি, নকশা সার্কেল-১, বাপাউবো, ঢাকা	সদস্য
১২.	প্রতিনিধি, প্রকল্প মূল্যায়ন পরিদপ্তর, বাপাউবো, ঢাকা	সদস্য
১৩.	সিনিয়র সহকারী প্রধান (সংশ্লিষ্ট), পরিকল্পনা কমিশন	সদস্য
১৪.	উপসচিব (পরিকল্পনা শাখা-২), পানি সম্পদ মন্ত্রণালয়	সদস্য সচিব

কার্যপরিধি :

- কমিটি চলমান কাজের স্থান ও ইতোমধ্যে সমাপ্ত কাজের স্থান পরিদর্শন করবেন এবং অনুমোদিত ডিপিপি অনুযায়ী গুণগতমান অক্ষম রেখে কাজ সম্পন্ন হয়েছে কিনা তা পরীক্ষা করবেন;
- কমিটি কাজের প্রয়োজনে যেকোন ধরনের পরিবর্তন/পরিমার্জনের প্রস্তাব করতে পারবেন;
- কমিটি স্টেক হোল্ডারের সাথে চলমান কাজের উদ্দেশ্য সম্পর্কে আলোচনা করবেন এবং উদ্ভূত সমস্যার বিষয়ে তাদের সাথে মত/অভিজ্ঞতা বিনিময় করবেন;
- কমিটি কাজের স্টেকহোল্ডারের সঙ্গে আলোচনা করে কাজটির ইতিবাচক এবং ক্ষতিকারক দিকগুলো চিহ্নিতপূর্বক সংশ্লিষ্ট মাঠ কর্মকর্তাদের সাথে আলোচনা মাধ্যমে দিক নির্দেশনামূলক মতামত প্রদান করবেন;
- কমিটি সর্বশেষ আইএমইডি প্রতিবেদনে দেওয়া তথ্যের সাথে বাস্তব অগ্রগতির তুলনা/মূল্যায়ন করবেন; এবং
- কমিটি বাপাউবোর সংশ্লিষ্ট মাঠ কর্মকর্তাদের সাথে কাজের অগ্রগতি নিয়ে আলোচনাপূর্বক সময়মত প্রকল্প শেষ করার জন্য প্রয়োজনীয় পদক্ষেপ গ্রহণের নিমিত্ত সুপারিশ করবেন।
- কমিটি প্রকল্পের কার্যক্রম পর্যবেক্ষণপূর্বক সুপারিশসহ এ মন্ত্রণালয়ের সিনিয়র সচিব মহোদয়ের নিকট একটি প্রতিবেদন পেশ করবে।

২.৪। মূল্যায়ন পদ্ধতি:

মধ্যবর্তী মূল্যায়নে নিম্নোক্ত পদ্ধতি অনুসরণ করা হয়েছে:

- মধ্যবর্তী মূল্যায়ন কমিটি কর্তৃক সর্বপ্রথম প্রকল্প দলিল, এডিপি/আরএডিপি এবং প্রকল্পের বিভিন্ন অগ্রগতি প্রতিবেদন নিয়ে আলোচনা ও পর্যালোচনা করা;
- কমিটির সদস্যবৃন্দ কর্তৃক প্রকল্পের কাজের বাস্তব অবস্থা পর্যবেক্ষণের জন্য দৈবচয়নের ভিত্তিতে প্রকল্প এলাকা পরিদর্শন এবং প্রকল্পের আওতায় ইতোমধ্যে বাস্তবায়িত ও বাস্তবায়নধীন কাজের তথ্য ও উপাত্ত সংগ্রহ করা;

- কমিটির সদস্যবৃন্দ কর্তৃক প্রকল্প এলাকা পরিদর্শনকালে প্রকল্পের উপকারভোগী, স্থানীয় জনপ্রতিনিধি এবং প্রকল্প সংশ্লিষ্ট কর্মকর্তাদের সাথে আলোচনা ও মতামত গ্রহণ;
- পরিদর্শনলব্ধ অভিজ্ঞতা, মাঠ পর্যায় থেকে প্রাপ্ত তথ্যাদি এবং প্রকল্প সংশ্লিষ্ট কর্মকর্তাদের মতামত ও বাংলাদেশ পানি উন্নয়ন বোর্ডের প্রকল্প কর্তৃপক্ষের দেয়া তথ্যাদির বিশ্লেষণ।

২.৫। মূল্যায়নের সীমাবদ্ধতা:

পানি সম্পদ মন্ত্রণালয়ের আওতায় বাংলাদেশ পানি উন্নয়ন বোর্ড কর্তৃক বাস্তবায়নাধীন “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প।” শীর্ষক প্রকল্পটি জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকায় যমুনা নদীর বাম তীরে অবস্থিত। প্রকল্পের অধীন ৬.২৫০ কি.মি. নদীতীর সংরক্ষণ এবং ২টি এন্ড টার্মিনেশন কাজের সংস্থান রয়েছে। প্রকল্পটির অনুমোদিত মোট ব্যয় ৫৮৪৭২.২৪ লক্ষ টাকা, যার শতভাগ জিওবি অনুদান। প্রকল্পটির মোট প্যাকেজ ২৩টি, যার মধ্যে ২২টি প্যাকেজ এর কাজ চলমান রয়েছে। প্রকল্প এলাকা সরেজমিন পরিদর্শনকালে প্রকল্পের দলিলাদি পর্যালোচনা, চলমান কাজের বিভিন্ন অগ্রগতি আলোচনা ও পর্যালোচনা, প্রকল্প পরিচালকসহ অন্যান্য সংশ্লিষ্ট কর্মকর্তা, সীমিত পর্যায়ে স্থানীয় জনগণ ও জনপ্রতিনিধিদের সাথে আলোচনাপূর্বক তাদের মতামতের ভিত্তিতে মূল্যায়ন প্রতিবেদন প্রণয়ন করা হয়েছে। মূল্যায়ন কমিটির কার্যপরিধিতে সময়ে সময়ে প্রকল্প এলাকা পরিদর্শনের বিষয় উল্লেখ থাকলেও সময়ের স্বল্পতার কারণে শুধুমাত্র একবার প্রকল্প এলাকা পরিদর্শন করা হয়।

তৃতীয় অধ্যায়

প্রকল্প এলাকা পরিদর্শন

৩.১। ভূমিকা:

মধ্যবর্তী মূল্যায়ন কমিটির সদস্যগণ গত ২৫-২৬ নভেম্বর, ২০২২ খ্রিঃ তারিখ প্রকল্প এলাকা সরেজমিন পরিদর্শন করেন। প্রকল্পটি জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুড়ি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামথল এলাকায় যমুনা নদীর বাম তীরে অবস্থিত। কমিটির সদস্যগণ কর্তৃক প্রকল্প এলাকার যমুনা নদীর বাম তীরে সংরক্ষণ কাজ, এন্ড টার্মিনেশন নির্মাণ কাজ পরিদর্শন করা হয়। প্রকল্প এলাকা পরিদর্শনকালে কমিটির সদস্যবৃন্দ প্রকল্পের উপকারভোগী, জনপ্রতিনিধি এবং প্রকল্প সংশ্লিষ্ট কর্মকর্তাদের সাথে আলোচনা করেন, তাদের মতামত নেন এবং বিভিন্ন তথ্য উপাত্ত সংগ্রহ করেন।

৩.২। প্রকল্প এলাকা পরিদর্শনের বিবরণ:


মধ্যবর্তী মূল্যায়ন কমিটি প্রকল্প এলাকাভুক্ত জামালপুর জেলার মাদারগঞ্জ উপজেলায় যমুনা নদীর বাম তীরে পাকেরদহ নামক স্থানে প্যাকেজ নং-BPW-Paker-01/20-21 এর অনুকূলে ৩০০ মিটার ও BPW-Paker-04/20-21 এর অনুকূলে ৩০০ মিটার, জামথল নামক স্থানে প্যাকেজ নং-BPW-Jamthal-12/20-21 এর অনুকূলে ৩৫০ মিটার, BPW-Jamthal-13/20-21 এর অনুকূলে ৩৫০ মিটার, প্যাকেজ নং-BPW-Jamthal-17/20-21 এর অনুকূলে ৩৫০ মিটার, প্যাকেজ নং-BPW-Jamthal-18/20-21 এর অনুকূলে ৩৫০ মিটার, প্যাকেজ নং-BPW-Jamthal-19/20-21 এর অনুকূলে ৩৫০ মিটার, প্যাকেজ নং-BPW-Jamthal-20/20-21 এর অনুকূলে ৩৫০ মিটার, প্যাকেজ নং-BPW-Jamthal-21/20-21 এর অনুকূলে ২৫০ মিটার ও প্যাকেজ নং-BPW-Jamthal-22/20-21 এর অনুকূলে ২৫০ মিটার মোট ৬২৫০ মিটার চলমান তীর প্রতিরক্ষামূলক কাজ এবং ১ টি এন্ড টার্মিনেশন নির্মাণ কাজ পরিদর্শন করেন। পরিদর্শকালে দেখা যায় চলমান কাজ সমূহ প্রায় ৪৬.১৮% সমাপ্ত হয়েছে। কাজ সমূহ সমাপ্তের ফলে মাদারগঞ্জ উপজেলার যমুনা নদী সংলগ্ন রাস্তা, বিদ্যমান বসতবাড়ি নদী ভাঙান ও বন্যা হতে রক্ষা পেয়েছে।

মাদারগঞ্জ উপজেলায় জামথল এলাকায় যমুনা নদীর বামতীরে নদীতীর প্রতিরক্ষামূলক কাজের স্লোপে ব্লক প্রেসিং কাজ ২টি প্যাকেজের সমাপ্ত হয়েছে এবং অবশিষ্ট ২০টি প্যাকেজের কাজ চলমান তা যথাযথ বলে প্রতীয়মান হয়েছে। পাকেরদহ ও জামথল নামক স্থানে তীর প্রতিরক্ষামূলক কাজ পরিদর্শন কালে স্থানীয় চেয়ারম্যান ও প্রকল্পের সুবিধাভোগী জনসাধারণ উপস্থিত ছিলেন। প্রকল্পটির ৪৬.১৮% সমাপ্ত হয়েছে। স্থানীয় জনসাধারণ জানান যে কাজটি করার ফলে মাদারগঞ্জ উপজেলা, হাট-বাজার, কয়েকটি গ্রাম নদী ভাঙনের ঝুঁকিমুক্ত হয়েছে। অবশিষ্ট অংশের কাজ বাস্তবায়নে উক্ত স্থানে ব্লক নির্মাণ কাজ কমিটি কর্তৃক পরিলক্ষিত হয়। এছাড়াও প্রকল্প এলাকা পরিদর্শন কালে কমিটির সদস্যগণের সাথে প্রকল্প পরিচালক ও পানি উন্নয়ন বোর্ডের মাঠ পর্যায়ের অন্যান্য কর্মকর্তাগণ উপস্থিত ছিলেন। ভিপিপিতে মোট প্যাকেজ সংখ্যা মোট ২৩টি। নভেম্বর, ২০২২ পর্যন্ত কার্যাদেশ প্রদান করা হয়েছে ২২টি।


৩.২.১। নদী তীর সংরক্ষণ কাজঃ

জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুড়ি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামথল এলাকায় যমুনা নদীর বাম তীরে (চাইনেজ কিঃমিঃ ০.০০০ হতে কিঃমিঃ ৬.২৫০) = ৬.২৫০ কিঃমিঃ দৈর্ঘ্যে তীর সংরক্ষণ কাজ চলমান রয়েছে। তীর সংরক্ষণ কাজের জন্য ব্লক তৈরীর লক্ষ্যে প্রস্তুতকৃত Block manufacture yard পরিদর্শন করা হয়। পরিদর্শনকালে ব্লক তৈরির

পাথর, বালু, সিমেন্ট পর্যবেক্ষণ করা হয়। পর্যবেক্ষণে দেখা যায়, অধিকাংশ ক্ষেত্রে ব্যবহৃত সিমেন্টের test report নাই। যে ব্যান্ডের সিমেন্ট দিয়ে নির্মাণ কাজ করা হচ্ছে সেই ব্যান্ডের সিমেন্টের test report নাই। অন্য ব্যান্ডের সিমেন্টের test report সাইটে রাখা হয়েছে। প্রস্তুতকৃত ব্লকের স্টেকসমূহ পরিদর্শন করা হয়। প্রকল্পের কাজের ভাটিতে নদী ভাঙান রয়েছে এবং BIWTA কর্তৃক সারিয়াকান্দি-জামখল ফেরীঘাট নির্মাণাধীন রয়েছে। প্রকল্পের কাজের কারিগরী কমিটির অনুমোদিত প্রতিবেদনের সুপারিশ মোতাবেক প্রকল্পের কাজের ভাটিতে (চেইনেজ কিঃমিঃ ৬.২৫০ হতে কিঃমিঃ ৬.৭৫০) = ৫০০ মিটার দৈর্ঘ্যে নদীতীর সংরক্ষণ কাজ বাস্তবায়ন করা প্রয়োজন। পরিদর্শনে দেখা যায়, BIWTA কর্তৃক নির্মাণাধীন ফেরীঘাট রক্ষার জন্য ৫০০ মিটার অতিরিক্ত নদীতীর সংরক্ষণ কাজ বাস্তবায়ন না করলে নির্মাণাধীন ফেরীঘাটের স্থায়ী থাকবে না। মধ্যবর্তী মূল্যায়ন কমিটির সদস্যগণ পরিদর্শনকালে স্থানীয় জনসাধারণ ও প্রকল্পের কাজের সুফলভোগীদের সাথে মতবিনিময় করেন।

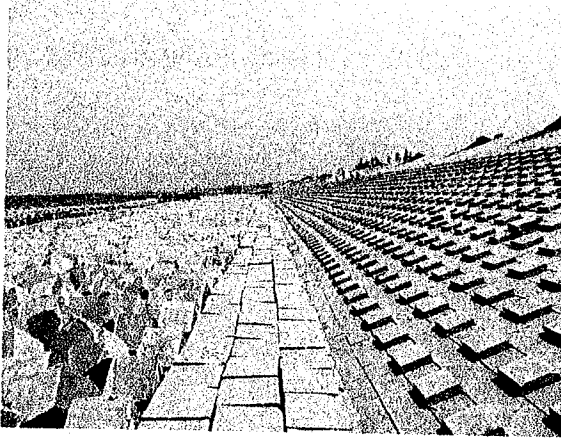

নদী তীর সংরক্ষণ কাজের ব্লক প্রেসিংকৃত অংশের স্থির চিত্র

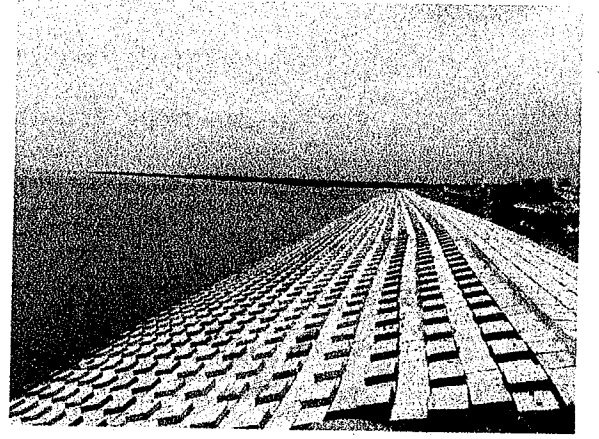

নদী তীর সংরক্ষণ কাজের ব্লক প্রেসিংকৃত অংশের স্থির চিত্র



চলমান কাজের জন্য প্রস্তুতকৃত ব্লকের সাইট পরিদর্শন



চলমান কাজের জন্য প্রস্তুতকৃত ব্লকের সাইট পরিদর্শন

Handwritten signatures and marks at the bottom of the page, including a large checkmark and several stylized signatures.



চলমান কাজের রকের স্টেকের স্থির চিত্র



চলমান কাজের রকের স্টেকের স্থির চিত্র



চলমান কাজের রক তৈরির পাথর পর্যবেক্ষণের স্থির চিত্র




চলমান কাজের রক তৈরির বালু পর্যবেক্ষণের স্থির চিত্র

৩.২.২। এন্ড টার্মিনেশন নির্মাণ কাজঃ

“জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প” শীর্ষক প্রকল্পের অধীনে প্যাকেজ নং- End Termination-US-05/20-21, End Termination-US-06/20-21, End Termination-US-07/20-21 এই ৩ টি প্যাকেজের সমন্বয়ে গঠিত তীর সংরক্ষণ কাজের উজানে ১ টি এন্ড টার্মিনেশন নির্মাণের কাজ চলমান রয়েছে। এছাড়া তীর সংরক্ষণ কাজের ভাটিতে ১ টি এন্ড টার্মিনেশন নির্মাণ কাজ প্যাকেজ নং- End Termination-DS-23/20-21 ডিপিসি সংশোধন সাপেক্ষে নির্মাণ করা হবে। প্রকল্পের ডিপিসি সংশোধনের পরে উক্ত কাজের টেন্ডার আহ্বান করা হবে।

Handwritten signatures and initials are present at the bottom of the page, including a large signature on the left and several smaller ones on the right.

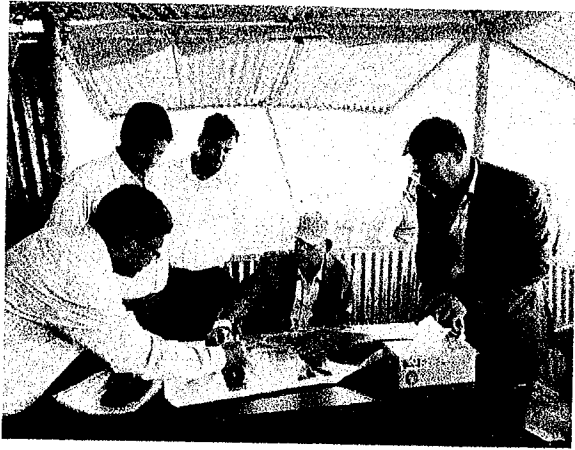

প্রকল্পের কাজের ডিজাইন পর্যবেক্ষণের স্থির চিত্র



চলমান কাজের ব্লক তৈরির সিমেন্ট পর্যবেক্ষণের স্থির চিত্র



চলমান কাজ পরিদর্শনের স্থির চিত্র



চলমান কাজ পরিদর্শনের স্থির চিত্র

Handwritten signatures and marks, including a checkmark, a circle, and various stylized initials and names.

চতুর্থ অধ্যায়

জনপ্রতিনিধি, প্রকল্প সংশ্লিষ্ট কর্মকর্তা এবং সুফলভোগীদের মতামত

৪.১। জনপ্রতিনিধির মতামত:

পরিদর্শনকালে স্থানীয় জনসাধারণ এবং জন প্রতিনিধিগণ মধ্যবর্তী মূল্যায়ন কমিটিকে জানান যে, প্রকল্পের কাজ আংশিক বাস্তবায়নের ফলে প্রকল্প এলাকার যে স্থানে নদীর তীর সংরক্ষণ কাজ বাস্তবায়ন করা হয়েছে ঐ এলাকায় ভাঙ্গণ বন্ধ হয়েছে। এই কাজ করার ফলে কৃষি জমির শস্যের নিবিড়তা বেড়েছে, বন্যা নিয়ন্ত্রণ এবং নিষ্কাশন ব্যবস্থার উন্নতি সাধিত হয়েছে। স্থানীয় জনসাধারণ ও স্থানীয় জনপ্রতিনিধিগণ যমুনা নদীর তীর সংরক্ষণ কাজ বাস্তবায়নের উপর গুরুত্বারোপ করেছেন।

৪.২। প্রকল্প সংশ্লিষ্ট কর্মকর্তাদের মতামত:

মধ্যমেয়াদী মূল্যায়ন কমিটি কর্তৃক পরিদর্শনকালে প্রকল্প সংশ্লিষ্ট কর্মকর্তা তত্ত্বাবধায়ক প্রকৌশলী, বাপাউবো, টাঙ্গাইল ও প্রকল্প পরিচালক “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা” শীর্ষক প্রকল্প; নির্বাহী প্রকৌশলী, জামালপুর পওর বিভাগ, বাপাউবো, জামালপুরসহ মাঠদপ্তরের অন্যান্য কর্মকর্তাগণ উপস্থিত ছিলেন। তাদের সাথে আলোচনা করে জানা যায় যে, প্রকল্পের আওতায় ইতোমধ্যে ৬.২৫০ কিলোমিটার নদী তীর সংরক্ষণ কাজের মধ্যে সম্পূর্ণ দৈর্ঘ্যে কাজ বাস্তবায়ন চলমান হয়েছে এবং ২ টি এন্ড টার্মিনেশন নির্মাণ কাজের মধ্যে ১ টি এন্ড টার্মিনেশন নির্মাণের কাজ চলমান রয়েছে, প্রকল্পের কাজের সার্বিক অগ্রগতি ৪৬.১৮%। নদী তীর সংরক্ষণ কাজ বাস্তবায়নের ফলে প্রকল্প এলাকার যে স্থানে নদীতীর সংরক্ষণ কাজ বাস্তবায়ন করা হয়েছে ঐ এলাকায় ভাঙ্গণ রোধ হয়েছে এবং প্রায় ১০০ হেক্টর ভূমি নদী ভাঙ্গণের কবল হতে রক্ষা পেয়েছে। বন্যা নিয়ন্ত্রণ এবং নিষ্কাশন ব্যবস্থার উন্নতি সাধিত হয়েছে।

৪.৩। সুফলভোগীদের মতামত:

প্রকল্পের প্রধান Stakeholder হলো জামালপুর জেলার মাদারগঞ্জ উপজেলা ও বগুড়া জেলার সারিয়াকান্দি উপজেলার সাধারণ জনগণ। এ বিষয়ে প্রকল্প পরিদর্শনকালীন সময়ে উপস্থিত এলাকাবাসীর সাথে আলোচনা হয়। আলোচনায় প্রকল্পের সুফলভোগীদের মতামত নিম্নরূপ :

১) নদী তীর সংরক্ষণ কাজ বাস্তবায়নের ফলে জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা সংলগ্ন বাজার, কৃষি জমি, স্কুল-কলেজ, মাদ্রাসা, বসতবাড়ী, মূল্যবান গাছপালা, সড়ক, সরকারী ও বেসরকারী মূল্যবান অবকাঠামো এবং গুরুত্বপূর্ণ স্থাপনাসমূহ নদী ভাঙ্গণের কবল হতে রক্ষা পেয়েছে;

২) নদীর গতি পথ পরিবর্তন প্রতিরোধ করা অনেকাংশে সম্ভব হয়েছে। ফলশ্রুতিতে প্রকল্প এলাকার নদী তীর অদ্যাবধি স্থিতিশীল অবস্থায় রয়েছে; প্রকল্পভুক্ত এলাকা নদী ভাঙন হতে রক্ষা পেয়েছে।

৩) বর্নিত এলাকায় নদী ভাঙ্গণ রোধ হওয়ায় বিরূপ প্রভাব হতে প্রকল্প এলাকার পরিবেশের ভারসাম্য রক্ষা পেয়েছে।

৪) নদী তীর সংরক্ষণ কাজ বাস্তবায়ন করার ফলে বর্ষায় প্রকল্প এলাকায় বন্যা নিয়ন্ত্রণ ও নিষ্কাশন ব্যবস্থার উন্নতি সাধিত হয়েছে।



চিত্র: সুফলভোগীদের সাথে আলোচনা

Handwritten signatures and marks, including a large 'P.' and several other stylized initials and marks.


পঞ্চম অধ্যায়
কমিটির পর্যবেক্ষণ ও সুপারিশ

৫.১। কমিটির পর্যবেক্ষণঃ

প্রকল্প দলিলাদি পর্যবেক্ষণ, সরেজমিনে প্রকল্প এলাকা পরিদর্শন, প্রকল্প সংশ্লিষ্ট কর্মকর্তাদের মতামত, জনপ্রতিনিধিদের মতামত এবং উপকারভোগীদের মতামতের ভিত্তিতে মধ্যবর্তী মূল্যায়ন কমিটির পর্যবেক্ষণসমূহ নিম্নরূপঃ

- ৫.১.১। প্রকল্পটি ৫৮৪৭২.২৪ লক্ষ টাকা ব্যয়ে (সম্পূর্ণ জিওবি) এপ্রিল, ২০২০ হতে জুন, ২০২৩ মেয়াদে বাস্তবায়নের জন্য বিগত ১০/০৩/২০২০ খ্রিঃ তারিখে অনুষ্ঠিত একনেক সভায় অনুমোদিত হয়েছে। অনুমোদিত ডিপিপি অনুযায়ী প্রকল্পের ভৌত কাজসমূহের মোট প্যাকেজ সংখ্যা ২৩ টি, যার মধ্যে ২২ টি প্যাকেজের কাজ চলমান রয়েছে এবং ০১ টি প্যাকেজের কাজ প্রকল্পের ডিপিপি সংশোধনের পরে টেন্ডার আহ্বানপূর্বক বাস্তবায়ন করা হবে। প্রকল্পের সার্বিক অগ্রগতি ৪৬.১৮%।
- ৫.১.২। প্রকল্পের ডিপিপিতে ৬.২৫০ কিঃমিঃ নদী তীর সংরক্ষণ কাজের সংস্থান রয়েছে। ৬.২৫০ কিলোমিটার নদী তীর সংরক্ষণ কাজের মধ্যে সম্পূর্ণ দৈর্ঘ্যে কাজ বাস্তবায়ন চলমান হয়েছে এবং ২ টি এন্ড টার্মিনেশন নির্মাণ কাজের মধ্যে ১ টি এন্ড টার্মিনেশন নির্মাণের কাজ চলমান রয়েছে।
- ৫.১.৩। মূল্যায়ন কমিটি কর্তৃক প্রথমে প্যাকেজ ১২ এর কাজ পরিদর্শন করা হয়। যমুনা নদীর বামতীরে সারিয়াকান্দি উপজেলার জামখল নামক স্থানে ২.৬ কিলোমিটার হতে ২.৯৫০ কিলোমিটার অর্থাৎ ৩৫০ মিটার নদীর তীর সংরক্ষণ কাজ প্যাকেজ ১২ এর আওতায় ২৬.১১ কোটি টাকা ব্যয়ে বাস্তবায়িত হচ্ছে। উক্ত প্যাকেজের বাস্তব অগ্রগতি ৩৭%। কনক্রিট casting এর জন্য Stone Chips এর সাইজ 40 mm down graded যথাযথ মনে হয়েছে। Concrete casting জন্য কোন প্রাটফরম তৈরী করা হয় নাই। সাইটে Fresh সিমেন্ট দিয়ে কাজ চলছে তবে কোন Test Report নাই। Fresh Cement দিয়ে কাজ চললেও সাইটে Premier Cement এর Test Report রাখা হয়েছে।
- ৫.১.৪। অতঃপর প্যাকেজ-১৪ এর নির্মাণ কাজ পরিদর্শন করা হয়। সারিয়াকান্দি উপজেলার জামখল নামক স্থানে যমুনা নদীর বামতীরে ৩.৩ কিলোমিটার হতে ৩.৬৫০ কিলোমিটার অর্থাৎ ৩৫০ মিটার নদীর তীর প্রতিরক্ষা কাজ প্যাকেজ ১৪-এর আওতায় ২৫.০৭ কোটি টাকা ব্যয়ে বাস্তবায়িত হচ্ছে। পরিদর্শনে দেখা যায়, Concrete ব্লকের গুণাগুণ BUET থেকে পরীক্ষা করানো হয়েছে যা সন্তোষজনক। তবে Concrete ব্লক তৈরীর জন্য কোন প্রাটফরম তৈরী করা হয় নাই। Concrete ব্লকের Finishing যথাযথ মান অর্জনের জন্য প্রাটফরম তৈরী করা প্রয়োজন। সাইটে Seven Ring ব্র্যান্ডের Cement দিয়ে নির্মাণ কাজ বাস্তবায়িত হচ্ছে কিন্তু সিমেন্ট Test এর কোন Report নাই। তবে Shah Cement এর Test Report সাইটে রাখা হয়েছে।
- ৫.১.৫। পরবর্তীতে মূল্যায়ন কমিটি কর্তৃক প্যাকেজ ১৭- এর কাজ পরিদর্শন করা হয়। সারিয়াকান্দি উপজেলার জামখল নামক স্থানে যমুনা নদীর বাম তীরে ৪.৩৫০ কিলোমিটার থেকে ৪.৭ কিলোমিটার পর্যন্ত অর্থাৎ ৩৫০ মিটার নদী তীর সংরক্ষণ কাজ প্যাকেজ ১৭-এর আওতায় ২৫.৬৫ কোটি টাকা ব্যয়ে বাস্তবায়িত হচ্ছে। উক্ত প্যাকেজের বাস্তব অগ্রগতি ৪৯%। পরিদর্শনে দেখা যায়, কনক্রিট ব্লকের গুণাগুণ BUET থেকে Test করানো হয়েছে যা সন্তোষজনক। তবে নির্মাণের জন্য সাইটে বিদ্যমান Stone chips-এর মধ্যে অনেক Dust বিদ্যমান। Stone chips কনক্রিট casting-এ ব্যবহারের পূর্বে ভালভাবে Sieve করতে হবে।

১৬



- ৫.১.৬। অতঃপর প্যাকেজ ২২-এর আওতায় বাস্তবায়নাধীন নির্মাণ কাজ পরিদর্শন করা হয়। জামালপুর জেলার মাদারগঞ্জ উপজেলার পাকেরদহ ও বালিজুরি নামক স্থানে যমুনা নদীর তীর সংরক্ষণ কাজ প্যাকেজ-২২ এর আওতায় ১৯.৪৬ কোটি টাকা ব্যয়ে বাস্তবায়িত হচ্ছে। উক্ত প্যাকেজের বাস্তব অগ্রগতি ৪০%। পরিদর্শনে দেখা যায়, Bengal ব্রান্ডের সিমেন্ট দিয়ে নির্মাণ কাজ বাস্তবায়িত হচ্ছে কিন্তু সাইটে কোন Test Report নাই। নির্মাণ কাজে ব্যবহৃত Stone Chips এর মধ্যে Shingles বিদ্যমান। Shingles দিয়ে Concrete Casting না করে Bounder ভাঙ্গা Stone Chips দিয়ে Concrete Casting করা প্রয়োজন।
- ৫.১.৭। এছাড়া প্রকল্প এলাকায় ২২টি প্যাকেজে কাজ বাস্তবায়নাধীন থাকলেও ১টি মাত্র সাইট অফিস বিদ্যমান। নির্মাণ কাজের গুণাগুণ যথাযথভাবে মনিটরিং করার জন্য অধিক সংখ্যক সাইট থাকা বাঞ্ছনীয়।
- ৫.১.৮। সাইটে অফিসে ড্রইং ডিজাইনসহ নির্মাণ সামগ্রীর গুণাগুণ পরীক্ষার রিপোর্ট সংরক্ষণ করা আবশ্যিক।
- ৫.১.৯। ডিপিপি অনুযায়ী প্রকল্পটি জুন ২০২৩ এ সমাপ্তির জন্য নির্ধারিত; কিন্তু প্রকল্পের শেষ প্রান্তে BIWTA কর্তৃক জামালপুর সিরাজগঞ্জ যাতায়াতের জন্য ফেরীঘাট নির্মাণের কাজ চলছে। ফেরীঘাটের স্থায়ীত্ব রক্ষার্থে ৫০০ মিটার অতিরিক্ত তীর সংরক্ষণ কাজ বাস্তবায়ন করা প্রয়োজন। এই ৫০০ মিটার অতিরিক্ত তীর সংরক্ষণ কাজ বাস্তবায়ন করতে হলে প্রকল্পের ডিপিপি সংশোধন করতে হবে। সংশোধিত ডিপিপি অনুযায়ী প্রকল্পের মেয়াদ ১ বছর বৃদ্ধি করে, জুন ২০২৪ এর মধ্যে আবশ্যিকভাবে সকল কাজ সমাপ্ত করার লক্ষ্যে অবশিষ্ট কার্যক্রম দ্রুত সম্পন্ন করতে হবে। এ বিষয়ে প্রকল্প পরিচালকসহ বাপাউবোর উর্ধ্বতন কর্মকর্তা কর্তৃক মনিটরিং কার্যক্রম জোরদার করা প্রয়োজন।

৫.১.৯। প্রকল্পের মাধ্যমে প্রাপ্ত উপকারিতা:

(ক) আর্থ সামাজিক প্রভাবঃ

প্রকল্পটি বাস্তবায়নের ফলে নদীর তীর ভাঙ্গণ বন্ধ হয়েছে এবং শস্য/সম্পদ হানি হ্রাস পেয়েছে। পানি সম্পদ ব্যবস্থাপনার উন্নয়নের দ্বারা খামার/ভূমির উন্নয়ন এবং কর্মসংস্থানের সুযোগ সৃষ্টি হয়েছে। প্রকল্প বাস্তবায়নের মাধ্যমে প্রকল্প এলাকার ফসল উৎপাদন বৃদ্ধির মাধ্যমে দারিদ্র্যতা হ্রাস পেয়ে আর্থিক স্বচ্ছলতা বৃদ্ধির সুযোগ সৃষ্টি হয়েছে।

(খ) পরিবেশগত প্রভাবঃ

পরিবেশের উপর কোন ঋণাত্মক প্রভাব নাই বরং নদী তীর সংরক্ষণ কাজ বাস্তবায়নের ফলে জীব বৈচিত্র্যের জন্য অনুকূল পরিবেশ সৃষ্টি হয়েছে। নদী ভাঙ্গণ বন্ধ হওয়ায় মৎস্যের অবাধ এবং নিরাপদ বিচরণের ক্ষেত্র সৃষ্টি হয়েছে ফলে মৎস্য উৎপাদন বৃদ্ধির সম্ভাবনা প্রসারিত হয়েছে। একই সাথে নদীপথে নৌ চলাচলের পথ সুগম হয়েছে।

১৭

৫.২। কমিটির সুপারিশঃ

৫.২.১। ৬.২৫০ কিলোমিটার নদী তীর সংরক্ষণ কাজের মধ্যে সম্পূর্ণ দৈর্ঘ্যে কাজ বাস্তবায়ন চলমান হয়েছে এবং ২ টি এন্ড টার্মিনেশন নির্মাণ কাজের মধ্যে ১ টি এন্ড টার্মিনেশন নির্মাণের কাজ চলমান রয়েছে। কাজ যথাসময়ে বাস্তবায়ন করা প্রয়োজন। প্রকল্প সমাপ্তির পর নিয়মিত বাজেট বরাদ্দের মাধ্যমে বাস্তবায়িত কাজের নিয়মিত রক্ষণাবেক্ষণ বজায় রাখতে হবে।

৫.২.২। নদীতীর সংরক্ষণ কাজ বাস্তবায়ন কাজ সমাপ্তির পরে ৬.২৫ কিঃমিঃ দৈর্ঘ্যে বৃক্ষরোপণ করতে হবে।

৫.২.৩। সিসি ব্লকের Finishing যথাযথ মানে অর্জনের লক্ষ্যে ব্লক তৈরির স্থানে platform তৈরী/ brick soling করা আবশ্যিক। যথাযথ মানের stone chips, বালি ও সিমেন্ট দিয়ে কনক্রিট casting করতে হবে।

৫.২.৪। নির্মাণ কাজে ব্যবহৃত নির্মাণ সামগ্রী অর্থাৎ পাথর, সিমেন্ট, বালু ও কংক্রিটের গুণাগুণ বাংলাদেশ প্রকৌশল বিশ্ববিদ্যালয় (বুয়েট) এর ল্যাবরেটরী থেকে পরীক্ষা করতে হবে এবং পরীক্ষায় প্রাপ্ত রিপোর্ট সাইটে সংরক্ষণ করতে হবে। যে ব্রান্ডের সিমেন্ট দিয়ে কাজ বাস্তবায়ন হবে সেই ব্রান্ডের সিমেন্টের গুণাগুণ পরীক্ষার রিপোর্ট সাইটে সংরক্ষণ করতে হবে।

৫.২.৫। প্রকল্প এলাকায় প্রকল্প কার্যক্রমের তথ্য সম্বলিত একাধিক সাইনবোর্ড লাগাতে হবে।

৫.২.৬। প্রকল্প এলাকায় কাজের দৈর্ঘ্য বিবেচনায় একাধিক সাইট অফিস থাকা বাঞ্ছনীয়। সাইট অফিসে ড্রয়িং ডিজাইন এ নির্মাণ সামগ্রী পরীক্ষার রিপোর্ট সংরক্ষণ করতে হবে।

৫.২.৭। প্রকল্পের কাজের ৫০০ মিটার দৈর্ঘ্য বৃদ্ধি ও ১ বছর মেয়াদ বৃদ্ধিজনিত কারনে ডিপিপি সংশোধনের কাজ দ্রুত সম্পন্ন করতে হবে এবং অনুমোদিত আরডিপিপি অনুযায়ী যাবতীয় কার্যক্রম সম্পন্ন করে প্রকল্পটি আবশ্যিকভাবে অনুমোদিত সময়ের মধ্যে সমাপ্ত করতে হবে।

৫.২.৮। প্রকল্প এলাকায় সাধারণ মানুষের ওঠানামার সুবিধার্থে মাঝে মাঝে কনক্রিট ব্লক দিয়ে ঘাটলা করতে হবে।

৫.২.৮। যথাযথ Specification এবং Design অনুযায়ী সঠিকভাবে কাজ বাস্তবায়নের বিষয়টি প্রকল্প কর্তৃপক্ষ নিশ্চিত করবে। নির্মাণ কাজের গুণাগুণ অবশ্যই নিশ্চিত করতে হবে।

৫.২.৯। প্রকল্প কাজ বাস্তবায়নের কাজ পূর্ব এবং কাজ পরবর্তী ছবি সংরক্ষণ করা প্রয়োজন যাতে বাস্তবায়িত কাজের ফলাফল ভালভাবে পর্যবেক্ষণ করা যায়। পাশাপাশি আধুনিক প্রযুক্তি ব্যবহারের মাধ্যমে প্রকল্প পরিচালকের দপ্তর থেকে প্রকল্পের কাজ পরিবীক্ষণের ব্যবস্থা রাখা যেতে পারে।

১৮



(হাবিবুল হাসান রুমি)
সিনিয়র সহকারী প্রধান
কৃষি, পানি সম্পদ ও পল্লী প্রতিষ্ঠান বিভাগ
পরিকল্পনা কমিশন
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি

(দ্বীন ইসলাম)
নির্বাহী প্রকৌশলী
জামালপুর পওর বিভাগ, জামালপুর
বাপাউবো
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি

(মো: নুরে হেলাল)
পরিচালক,
প্রকল্প মূল্যায়ন পরিদপ্তর
বাপাউবো
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি

(মো: আরিফ হোসেন)
নির্বাহী প্রকৌশলী
ডিজাইন সার্কেল-১
বাপাউবো
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(পলাশ কুমার ব্যানার্জী)
নির্বাহী প্রকৌশলী
চীফ মনিটরিং এর দপ্তর
বাপাউবো
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(নাজমুল ইসলাম ভূঁইয়া)
উপ সচিব (উন্নয়ন শাখা-৩)
পানি সম্পদ মন্ত্রণালয়
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(খায়রুন নাহার)
উপ সচিব (পরিকল্পনা শাখা-২)
পানি সম্পদ মন্ত্রণালয়
ও সদস্য সচিব, মধ্যবর্তী মূল্যায়ন কমিটি।

(মুহাম্মদ সিরাজুল ইসলাম)
তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক
বাপাউবো, টাঙ্গাইল
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(মোঃ শহীদুল ইসলাম)
উপ-প্রধান (পানি সম্পদ)
কৃষি, পানি সম্পদ ও পল্লী প্রতিষ্ঠান বিভাগ
পরিকল্পনা কমিশন
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(এ, এইচ, এম, আনোয়ার পাশা)
উপ-প্রধান, পরিকল্পনা অধিশাখা-১
পানি সম্পদ মন্ত্রণালয়
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(দীপাঙ্কিতা সাহা)
মুখ্য সচিব (উন্নয়ন-২ অধিশাখা)
পানি সম্পদ মন্ত্রণালয়
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(জনাব মো: সাইফুল ইসলাম)
মহাপরিচালক,
আইএমইডি
ও সদস্য, মধ্যবর্তী মূল্যায়ন কমিটি।

(মহাঃ এনা মূল হক)
মুখ্যপ্রধান (সেচ উইং)
কৃষি, পানি সম্পদ ও পল্লী প্রতিষ্ঠান বিভাগ
পরিকল্পনা কমিশন
ও সহ-আহবায়ক, মধ্যবর্তী মূল্যায়ন কমিটি।

(এস, এম, রেজাউল মোস্তফা কামাল)
অতিরিক্ত সচিব (পরিকল্পনা)
পানি সম্পদ মন্ত্রণালয়
ও আহবায়ক, মধ্যবর্তী মূল্যায়ন কমিটি।

Office of the
Accounts Officer
Regional Accounting Centre
BWDB, Mymensingh.
Tel.(Off)-091-63002
E-mail: mymenrac@gmail.com



বাংলাদেশ পানি উন্নয়ন বোর্ড

হিসাবরক্ষণ কর্মকর্তার কার্যালয়
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।
ফোন(অফিস)-০৯১-৬৩০০২

স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-৪/৪৩

তারিখঃ ০৩-০৮-২০২১ খ্রিঃ।

বরাবর

প্রকল্প পরিচালক
“জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন
পাকেরদহ ও বালিজুরি ইউনিয়ন এবং বগুড়া
জেলার সারিয়াকান্দি উপজেলাধীন জামখল
এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প”

ও

তত্ত্বাবধায়ক প্রকৌশলী
ময়মনসিংহ পওর সার্কেল
বাপাউবো, ময়মনসিংহ।

বিষয়ঃ ২০২০-২১ অর্থ বৎসরের “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প” এর অব্যয়িত (Unspent) অর্থ জমাদান ও তার হিসাব বিবরণী প্রেরণ প্রসঙ্গে।

সূত্রঃ ১. পরিচালক, অর্থ পরিদপ্তর, বাপাউবো, ঢাকা-এর স্মারক নং-পাউবো, অর্থ (উবাত)/৭৪১/১ তারিখঃ ২২-০৬-২০২১ খ্রিঃ।

২. অত্র দপ্তরের স্মারক নং র্যাক/ময়মন/পাউবো/এফ-৪/৩৫ তারিখঃ ০৩/০৮/২০২১ খ্রিঃ

মহোদয়

যথাযথ সম্মান প্রদর্শন পূর্বক উপর্যুক্ত বিষয় ও সূত্র সমূহের আলোকে জানানো যাইতেছে যে, অত্র দপ্তরের পরিশোধ আওতাধীন দপ্তর জামালপুর পওর বিভাগ কর্তৃক বাস্তবায়িত “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প (প্রকল্প কোড নং-২২৪৩১৪১০০)” এর ২০২০-২১ অর্থ বৎসরের অব্যয়িত অর্থ ৯৫,৯৬,১৫৯.০০ টাকা রূপালী ব্যাংক লিমিটেড, ছোট বাজার শাখা, ময়মনসিংহ হইতে পরিচালক, অর্থ, বাপাউবো, ঢাকা এর প্রকল্পের হিসাব নং-এসএনডি-২৯০৫১০২০০১৩৮৭, পূবালী ব্যাংক লিমিটেড, ফরেন এক্সচেঞ্জ শাখা, ঢাকায় বিইএফটিএন পদ্ধতিতে স্থানান্তর করা হইয়াছে। উক্ত প্রকল্পের অর্থনৈতিক কোড অনুযায়ী অব্যয়িত অর্থের হিসাব বিবরণী আপনার সদয় পরবর্তী প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্তে এতদসঙ্গে প্রেরণ করা হইল।

সংযুক্তি ৪-

১. অর্থনৈতিক কোড অনুযায়ী অব্যয়িত অর্থের হিসাব বিবরণী-০১ (এক) খানা।

আপনার অনুগত

মোহাম্মদ ফারুক চৌধুরী
হিসাব রক্ষণ কর্মকর্তা
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।

তারিখঃ ০৩-০৮-২০২১ খ্রিঃ।

স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-৪/৪৩/১(৭)

সদয় অবগতি/অবগতি ও প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্তে অনুলিপি প্রেরণ করা হইল ৪-


- ১। অতিরিক্ত মহাপরিচালক, অর্থ, বাপাউবো, ঢাকা।
- ২। প্রধান প্রকৌশলী, কেন্দ্রীয় অঞ্চল, বাপাউবো, ঢাকা।
- ৩। পরিচালক, হিসাব রক্ষণ পরিদপ্তর, বাপাউবো, ঢাকা।
- ৪। পরিচালক, অর্থ পরিদপ্তর, বাপাউবো, ঢাকা।
- ৫। পরিচালক, কার্যক্রম পরিদপ্তর, বাপাউবো, ঢাকা।
- ৬। নির্বাহী প্রকৌশলী, জামালপুর পওর বিভাগ, বাপাউবো, জামালপুর।
- ৭। পি এ টু মহাপরিচালক, বাপাউবো, ঢাকা।
- ৮। দপ্তর কপি।


হিসাব রক্ষণ কর্মকর্তা
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।

তারিখঃ ০৩/০৮/২১

Regional Accounting Center, BWDB, Mymensingh
Statement of Unspent Balance for Matharganj-Jamthal Project
For the Year Ended June 30, 2021 & FY 2020-21

Sl N o.	Description	Fund YTD Tk	Expenditure YTD Tk	Unspent YTD Tk	Remarks
1	2	3	4	5 (=3-4)	6
1	3111332-Madarganj-Jamthal &Pakerdhaha-Balijuri-I Honorarium	100,000.00	99,500.00	500.00	
2	3241101-Madarganj-Jamthal &Pakerdhaha-Balijuri-TA	100,000.00	95,731.00	4,269.00	
3	3243101-Madarganj-Jamthal &Pakerdhaha-Balijuri-POL	250,000.00	210,040.00	39,960.00	
4	3255102-Madarganj-Jamthal &Pakerdhaha-Balijuri-Printing	50,000.00	49,920.00	80.00	
5	3255105-Madarganj-Jamthal &Pakerdhaha-Balijuri-Stationery	100,000.00	99,995.00	5.00	
6	3257104-Madarganj-Jamthal &Pakerdhaha-Balijuri-Survey	200,000.00	199,760.00	240.00	
7	3258101-Madarganj-Jamthal &Pakerdhaha-Balijuri-M.V-PLD	75,000.00	74,950.00	50.00	
8	3258101-Madarganj-Jamthal &Pakerdhaha-Balijuri-M.V-XIEN	75,000.00	74,950.00	50.00	
9	3258103-Madarganj-Jamthal &Pakerdhaha-Balijuri-Computer	50,000.00	49,650.00	350.00	
	Sub_Total_Revenue	1,000,000.00	954,496.00	45,504.00	
10	4111321-Madarganj-Jamthal &Pakerdhaha-Balijuri-P Work	169,270,000.00	169,219,345.00	50,655.00	
11	4112101-Madarganj-Jamthal &Pakerdhaha-Balijuri-Jeep	9,500,000.00		9,500,000.00	
12	4112202-Madarganj-Jamthal &Pakerdhaha-Balijuri-Computer	80,000.00	80,000.00	-	
13	4112310-Madarganj-Jamthal &Pakerdhaha-Balijuri-Photocopier	150,000.00	150,000.00	-	
	Sub_Total_Capital	179,000,000.00	169,449,345.00	9,550,655.00	
	Project Total Code 224314100 Madarganj-Jamthal	180,000,000.00	170,403,841.00	9,596,159.00	


 Md. Faruk Chowdhury
 Accounts Officer
 RAC, BWDB
 Mymensingh


 03/08/21
 21



বাংলাদেশ পানি উন্নয়ন বোর্ড



হিসাবরক্ষণ কর্মকর্তার কার্যালয়
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।
ফোন(অফিস)-০৯১-৬৩০০২

স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-৪/১৪৫৪

তারিখঃ ৩০-০৬-২০২২ খ্রিঃ।

বরাবর

প্রকল্প পরিচালক

“জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন
পাকেরদহ ও বালিজুরি ইউনিয়ন এবং বগুড়া
জেলার সারিয়াকান্দি উপজেলাধীন জামখল
এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প”

ও

তত্ত্বাবধায়ক প্রকৌশলী

টাকাইল পানি উন্নয়ন সার্কেল

বাপাউবো, টাকাইল।

বিষয়ঃ ২০২১-২২ অর্থ বৎসরের “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প” এর অব্যয়িত (Unspent) অর্থ জমাদান ও তার হিসাব বিবরণী প্রেরণ প্রসঙ্গে।

- সূত্রঃ ১. পরিচালক, অর্থ পরিদপ্তর, বাপাউবো, ঢাকা-এর স্মারক নং-পাউবো, অর্থ (উভাত)/৮৫৬ তারিখঃ ১৯-০৬-২০২২ খ্রিঃ।
২. অত্র দপ্তরের স্মারক নং র্যাক/ময়মন/পাউবো/এফ-৪/১৪৪১ তারিখঃ ৩০-০৬-২০২২ খ্রিঃ।

মহোদয়

যথাযথ সম্মান প্রদর্শন পূর্বক উপর্যুক্ত বিষয় ও সূত্র সমূহের আলোকে জানানো যাইতেছে যে, অত্র দপ্তরের পরিশোধ আওতাধীন দপ্তর জামালপুর পওর বিভাগ কর্তৃক বাস্তবায়িত “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প (প্রকল্প কোড নং-২২৪৩১৪১০০)” এর ২০২১-২২ অর্থ বৎসরের অব্যয়িত অর্থ ৪৪,৩৯,৭৭১.০০ টাকা রূপালী ব্যাংক লিমিটেড, ছোট বাজার শাখা, ময়মনসিংহ হইতে পরিচালক, অর্থ, বাপাউবো, ঢাকা এর প্রকল্পের হিসাব নং-এসএনডি-২৯০৫১০২০০১৩৮৭, পূবালী ব্যাংক লিমিটেড, ফরেন এক্সচেঞ্জ শাখা, ঢাকায় বিইএফটিএন পদ্ধতিতে স্থানান্তর করা হইয়াছে। উক্ত প্রকল্পের অর্থনৈতিক কোড অনুযায়ী অব্যয়িত অর্থের হিসাব বিবরণী আপনার সদয় পরবর্তী প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্তে এতদসঙ্গে প্রেরণ করা হইল।

সংযুক্তি ৪-

১. অর্থনৈতিক কোড অনুযায়ী অব্যয়িত অর্থের হিসাব বিবরণী-০১ (এক) খানা।
২. অব্যয়িত অর্থ স্থানান্তরের কপি-০১ (এক) খানা।
৩. ব্যাংক বিবরণী-০১ (এক) খানা।

আপনার অনুগত

মোহাম্মদ ফারুক চৌধুরী
হিসাব রক্ষণ কর্মকর্তা
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।

তারিখঃ ৩০-০৬-২০২২ খ্রিঃ।

স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-৪/১৪৫৪/১(৬)

সদয় অবগতি/অবগতি ও প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্তে অনুলিপি প্রেরণ করা হইল ৪-

- ১। অতিরিক্ত মহাপরিচালক, অর্থ, বাপাউবো, ঢাকা।
- ২। প্রধান প্রকৌশলী, কেন্দ্রীয় অঞ্চল, বাপাউবো, ঢাকা।
- ৩। পরিচালক, হিসাব রক্ষণ পরিদপ্তর, বাপাউবো, ঢাকা।
- ৪। পরিচালক, অর্থ পরিদপ্তর, বাপাউবো, ঢাকা (সংযুক্তিসহ)।
- ৫। পরিচালক, কার্যক্রম পরিদপ্তর, বাপাউবো, ঢাকা।
- ৬। নির্বাহী প্রকৌশলী, জামালপুর পওর বিভাগ, বাপাউবো, জামালপুর (সংযুক্তিসহ)।
- ৭। দপ্তর কপি।

Regional Accounting Center, BWDB, Mymensingh
Statement of Unspent Balance for Jamnal Project (Proj Code- 224314100) Under Jamalpur O&M Division
For the Year Ended June 30, 2022 & FY 2021-22

Sl No.	Code & description	Fund received		Expenditure		Unspent		Transfer by BEFTN system
		YTD	Tk	YTD	Tk	YTD	Tk	
1	3111332-Honorarium	1,300,000.00		308,500.00		991,500.00		Our M. No.1441 Dt-30.6.22
2	3241101-T.V	50,000.00		49,182.00		818.00		
3	3243101-Petrol & Lubricant	200,000.00		192,542.00		7,458.00		
4	3255101-Computer consumables	100,000.00		99,900.00		100.00		
5	3255102-Printing & Binding	100,000.00		99,855.00		145.00		
6	3255105-Other Stationery	50,000.00		49,690.00		310.00		
7	3257104-Survey	200,000.00		199,760.00		240.00		
8	3258101-ALV	100,000.00		99,150.00		850.00		
9	3258103-Computer	100,000.00		99,900.00		100.00		
	Sub Total Revenue	2,200,000.00		2,198,479.00		1,001,521.00		
10	4111321-Protective Work	638,100,000.00		638,061,333.00		38,167.00		
11	4112101-Jeep Purchases	9,500,000.00		6,100,000.00		3,400,000.00		
12	4112314-Office Furniture	200,000.00		199,917.00		83.00		
	Grand Total	650,000,000.00		645,560,229.00		3,438,250.00		
						4,439,771.00		

[Signature]
 Afd. Faruk Chowdhury
 Accounts Officer

R.V.C., BWDB

Mymensingh

[Signature]
 30/6/22

Office of the
Accounts Officer
Regional Accounting Centre
BWDB, Mymensingh.
Tel.(Off)-091-63002
E-mail: mymenrac@gmail.com



বাংলাদেশ পানি উন্নয়ন বোর্ড

হিসাবরক্ষণ কর্মকর্তার কার্যালয়
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।
ফোন(অফিস)-০৯১-৬৩০০২

স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-১/১৪৮৩

তারিখঃ ২৬-০৬-২০২৩ খ্রিঃ।

বরাবর

পরিচালক

অর্থ পরিদপ্তর

বাপাউবো, ঢাকা।

বিষয়ঃ ২০২২-২৩ অর্থ বৎসরে উন্নয়ন প্রকল্প খাতের অব্যয়িত (Unspent) অর্থ জমাদান ও তার হিসাব বিবরণী প্রেরণ প্রসঙ্গে।

- সূত্রঃ ১. আপনার দপ্তর স্মারক নং-পাউবো (অর্থ) উবাত/৯০৯, তারিখঃ ২১-০৬-২০২৩ খ্রিঃ।
২. অত্র দপ্তরের স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-১/১৪৭৪ তারিখঃ ২৬-০৬-২০২৩ খ্রিঃ।

মহোদয়

যথাযথ সম্মান প্রদর্শন পূর্বক উপর্যুক্ত বিষয় ও সূত্র সমূহের আলোকে জানানো যাইতেছে যে, অত্র দপ্তরের পরিশোধ আওতাধীন দপ্তর সমূহের ২০২২-২৩ অর্থ বৎসরের জামালপুর পওর বিভাগের মাদারগঞ্জ জামখল প্রকল্পের (কোড-২২৪৩১৪১০০)-এর অব্যয়িত অর্থ ৫৫,৪২৮.০০, কিশোরগঞ্জ পানি উন্নয়ন বিভাগের মিঠামইন প্রকল্পের (কোড-২২৪২৫০৭০০)-এর অব্যয়িত অর্থ ১০,১৬৬.০০ ও দশ উপজেলা প্রকল্পের (কোড-২২৪৩৫৯৫০০)-এর অব্যয়িত অর্থ ১২,১৭৯.০০ এবং নেত্রকোনা পওর বিভাগের বারহাটা প্রকল্পের (কোড-২২৪৩৭০৭০০)-এর অব্যয়িত অর্থ ৩৫,৩৮,৮০০.০০ ও পূর্বধলা প্রকল্পের (কোড-২২৪৩৬১১০০)-এর অব্যয়িত অর্থ ১,০৭,৩৮৭.০০ টাকাসহ সর্বমোট ৩৭,২৩,৯৬০.০০ টাকা প্রকল্পের সংশ্লিষ্ট হিসাবে বিইএফটিএন পদ্ধতিতে স্থানান্তর করা হইয়াছে। উক্ত প্রকল্প সমূহের অব্যয়িত অর্থের হিসাব বিবরণী, ব্যাংক বিবরণীসহ অন্যান্য প্রয়োজনীয় কাগজ-পত্রাদি আপনার সদয় পরবর্তী প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্তে এতদসঙ্গে প্রেরণ করা হইল।

সংযুক্তি :-

১. সকল প্রকল্পের পৃথক পৃথক অব্যয়িত অর্থের হিসাব বিবরণী- ০১ (এক) খানা।
২. ব্যাংক বিবরণী- ০১ (এক) খানা।
৩. অব্যয়িত তহবিল স্থানান্তরের পত্র কপি- ০১ (এক) খানা।
৪. জাবোদা কপি- ০১ (এক) খানা।

আপনার অনুগত

মোহাম্মদ ফারুক চৌধুরী

হিসাব রক্ষণ কর্মকর্তা

আঞ্চলিক হিসাব কেন্দ্র

বাপাউবো, ময়মনসিংহ।

তারিখঃ ২৬-০৬-২০২৩ খ্রিঃ।

স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-৪/১৪৮৩/১(১০)

সদয় অবগতি/অবগতি ও প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্তে সংযুক্তিসহ অনুলিপি প্রেরণ করা হইলঃ

- ১। অতিরিক্ত মহাপরিচালক, অর্থ, বাপাউবো, ঢাকা।
- ২। প্রধান প্রকৌশলী, কেন্দ্রীয় অঞ্চল, বাপাউবো, ঢাকা।
- ৩। পরিচালক, হিসাব রক্ষণ পরিদপ্তর, বাপাউবো, ঢাকা।
- ৪। তত্ত্বাবধায়ক প্রকৌশলী, ময়মনসিংহ পওর সার্কেল, বাপাউবো, ময়মনসিংহ।
- ৫। তত্ত্বাবধায়ক প্রকৌশলী, টাঙ্গাইল পানি উন্নয়ন সার্কেল, বাপাউবো, টাঙ্গাইল।
- ৬-৮। নির্বাহী প্রকৌশলী ময়মনসিংহ/জামালপুর/নেত্রকোনা পওর বিভাগ, বাপাউবো, ময়মনসিংহ/জামালপুর/নেত্রকোনা।
- ০৯-১০। নির্বাহী প্রকৌশলী, টাঙ্গাইল/কিশোরগঞ্জ পানি উন্নয়ন বিভাগ, বাপাউবো, টাঙ্গাইল/কিশোরগঞ্জ।
- ১১। দপ্তর কপি।

হিসাব রক্ষণ কর্মকর্তা
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।

Regional Accounting Center, BWDB, Mymensingh
Statement of Fund & Expenditure of ADP
Financial Year 2022-2023
Dated on June-26, 2023

Sl No.	Project Name & Code and Office Name	Economic Code		Fund	Expenditure		Unspent	Remarks
		New	Name		GOB	GOB	GOB	
05	Madarganj-jamtal Pakerdhaha-Balijuri Project Code-224314100 Jamalpur O & M Div.	3111332 3111332	Honorarium (NTE) Honorarium (PSC/TEC/PIG) TA	1,000,000.00	986,014.00	13,986.00		
		3241101	Petrol & Lubricant	25,000.00	24,920.00	80.00		
		3243101	Computer consumables	77,000.00	59,425.00	17,575.00		
		3255101	Printing & Binding	50,000.00	49,900.00	100.00		
		3255102	Other Stationery	50,000.00	49,960.00	40.00		
		3257104	Survey	25,000.00	25,000.00	-		
		3258101	M.V.-XEN	100,000.00	99,433.00	567.00		
		3258103	Computer	48,000.00	24,920.00	23,080.00		
			Sub Total Revenue	50,000.00	50,000.00	-		
		4112101	Deep Purchases	1,425,000.00	1,369,572.00	55,428.00		
		4111321	Protective Work (0.00-6.250)	1,448,500,000.00	1,448,500,000.00	-		
		4111321	Protective Work (0.00-6.250) & 6.250 =128 M-End Termination	150,000,000.00	150,000,000.00	-		
			Sub Total Capital	1,598,500,000.00	1,598,500,000.00	-		
			Project Total_Madarganj	1,599,925,000.00	1,599,869,572.00	55,428.00		

Unspent amount Tk 55,428.00 transferred to FAC by EFTN system
Our M.No.-1483 dt-26.6.23

MD. Faruk Chowdhury
AO, RAC, BWDB
Mymensingh
26/6/23

Office of the
Accounts Officer
Regional Accounting Centre
BWDB, Mymensingh.
Tel.(Off)-091-63002
E-mail: mymenrac@gmail.com



বাংলাদেশ পানি উন্নয়ন বোর্ড

হিসাবরক্ষণ কর্মকর্তার কার্যালয়
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।
ফোন(অফিস)-০৯১-৬৩০০২

স্মারক নং- র্যাক/ময়মন/পাউবো/এফ-৪/১২২৬

তারিখঃ ৩০-০৬-২০২৪ খ্রিঃ

বরাবর

উপ-মহাব্যবস্থাপক
রূপালী ব্যাংক পিএলসি
হোটেল বাজার কর্পোরেট শাখা
ময়মনসিংহ।

বিষয়: বিইএফটিএন-এর মাধ্যমে অর্থ স্থানান্তর প্রসঙ্গে।

সূত্র: পরিচালক, অর্থ পরিদপ্তর, বাপাউবো, ঢাকা-এর স্মারক নং-পাউবো, (অর্থ) উবাত/৮৬৫ তারিখঃ ১৩-০৬-২০২৪ খ্রিঃ।

প্রিয় মহোদয়

সৌজন্য সহকারে জানানো যাইতেছে যে, ২০২৩-২৪ অর্থ বৎসরের উন্নয়ন প্রকল্পের অব্যয়িত জেরের অর্থ আপনার ব্যাংক শাখায় পরিচালিত অত্র দপ্তরের ব্যাংক হিসাব নম্বর এসএনডি-০৭৮৬০২৪৩২০১০১ (জিওবি) হইতে ৩ নং কলামে বর্ণিত বর্ণনানুসারে ৪ নং কলামে বর্ণিত পরিমাণ অর্থ পৃথক পৃথক ভাবে বিইএফটিএন এর মাধ্যমে আদায় স্থানান্তর করতঃ অত্র দপ্তরকে অবহিত করার জন্য বিশেষভাবে অনুরোধ করা হইল।

ক্র নং	যে হিসাব নম্বর হইতে স্থানান্তরিত হইবে	যে হিসাবের শিরোনাম, প্রকল্পের নাম, হিসাব নম্বর ও ব্যাংক শাখার অনুকূলে স্থানান্তর করিতে হইবে।	টাকার পরিমাণ	মন্তব্য
১।	এসএনডি- ০৭৮৬০২৪৩২০১০১ (জিওবি)	পরিচালক, অর্থ, বাপাউবো, ঢাকা হিসাব নং-এসএনডি-০১২৩০০০০০১৪৮৫ ওয়ান ব্যাংক লিমিটেড, কাওরান বাজার শাখা, ঢাকা, বাংলাদেশ। "কিশোরগঞ্জ জেলার ১০টি উপজেলায় নদীতীর প্রতিরক্ষা কাজ, ওয়েড প্রটেকশন ও খাল পুনঃখনন"।	৬৬,৩৬৮.০০	প্রকল্পের নামঃ কিশোরগঞ্জ ১০ উপজেলা। প্রকল্প কোড নং-২২৪৩৫৯৫০০। কিশোরগঞ্জ পানি উন্নয়ন বিভাগ।
২।	এসএনডি- ০৭৮৬০২৪৩২০১০১ (জিওবি)	পরিচালক, অর্থ, বাপাউবো, ঢাকা হিসাব নং-এসএনডি-২৯০৫১০২০০১৩৮৭ পূবালী ব্যাংক লিমিটেড, ফরেন এক্সচেঞ্জ শাখা, ঢাকা, বাংলাদেশ। "জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিজুরি ইউনিয়ন এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প"।	১৯,৪১৮.০০	প্রকল্পের নামঃ জামখল। প্রকল্প কোড নং-২২৪৩১৪১০০ জামালপুর পওর বিভাগ।
৩।	এসএনডি- ০৭৮৬০২৪৩২০১০১ (জিওবি)	পরিচালক, অর্থ, বাপাউবো, ঢাকা হিসাব নং-এসএনডি-০১০০২৪৪৭১০৯১৮ জনতা ব্যাংক লিমিটেড, গ্রীণরোড কর্পোরেট শাখা, ঢাকা, বাংলাদেশ। "নেত্রকোণা জেলার পূর্বধলা উপজেলার সেচ ও নিষ্কাশন ব্যবস্থার উন্নয়ন"।	১৫,৭৫,১৯২.০০	প্রকল্পের নামঃ পূর্বধলা। প্রকল্প কোড নং-২২৪৩৬১১০০। নেত্রকোণা পওর বিভাগ।
৪।	এসএনডি- ০৭৮৬০২৪৩২০১০১ (জিওবি)	পরিচালক, অর্থ, বাপাউবো, ঢাকা হিসাব নং-এসএনডি-০০৮৩৬০০০৭৩৬ ব্যাংক এশিয়া লিমিটেড, এমসিবি দিলকুশা শাখা, ঢাকা, বাংলাদেশ। "নেত্রকোণা জেলার সদর ও বারহাটা উপজেলায় বাঘরুয়া কর্ণপুর গ্রাম কংশ নদীর ভাঙ্গন হতে রক্ষা"।	১২,৮৩,০২২.০০	প্রকল্পের নামঃ নেত্রকোণা সদর ও বারহাটা। প্রকল্প কোড নং-২২৪৩৭০৭০০। নেত্রকোণা পওর বিভাগ।
৫।	এসএনডি- ০৭৮৬০২৪৩২০১০১ (জিওবি)	প্রকল্প পরিচালক, ৬৪ টি জেলার অভ্যন্তরস্থ হোটেল নদী, খাল এবং জলাশয় পুনঃখনন প্রকল্প, (১ম পর্যায়) হিসাব নং-এসএনডি-০০২৬০২৪০০০১৮০ "রূপালী ব্যাংক লিমিটেড, রূপালী সদন, মতিঝিল শাখা, ঢাকা।	৭৩,৩৯,৭১৭.০০	প্রকল্পের নামঃ ৬৪ জেলা। প্রকল্প কোড নং-২২৪২৫১৯০০
মোট =			১,০২,৮৩,৭১৭.০০	

কথায়: টাকা-এক কোটি দুই লক্ষ তিরিশি হাজার সাতশত সতের মাত্র।

আপনার বিশ্বস্ত

মোঃ ইমামুজ্জামান
৩০.০৬.২৪

হিসাবরক্ষক
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।

AL Mamun
৩০.০৬.২৪
আল মামুন

হিসাবরক্ষণ কর্মকর্তা
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।

স্মারক নং-র্যাক/ময়মন/পাউবো/এফ-৪/১২২৬/১(১২)

তারিখঃ ৩০-০৬-২০২৪ খ্রিঃ।

সদয় অবগতি/অবগতি ও প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্তে অনুলিপি প্রেরণ করা হইলঃ

- ১। অতিরিক্ত মহাপরিচালক, অর্থ, বাপাউবো, ঢাকা।
- ২। প্রধান প্রকৌশলী, কেন্দ্রীয় অঞ্চল, বাপাউবো, ঢাকা।
- ৩। নিয়ন্ত্রক (অহিনি), বাপাউবো, ঢাকা।
- ৪। পরিচালক(অহিনি), অর্থ পরিদপ্তর, বাপাউবো, ঢাকা।
- ৫। পরিচালক(অহিনি), হিসাব রক্ষণ পরিদপ্তর, বাপাউবো, ঢাকা।
- ৬। পরিচালক, কার্যক্রম পরিদপ্তর, বাপাউবো, ঢাকা।
- ৭। তত্ত্বাবধায়ক প্রকৌশলী, ময়মনসিংহ পওর সার্কেল, বাপাউবো, ময়মনসিংহ।
- ৮। তত্ত্বাবধায়ক প্রকৌশলী, টাঙ্গাইল পানি উন্নয়ন সার্কেল, বাপাউবো, টাঙ্গাইল।
- ৯-১২। নির্বাহী প্রকৌশলী, ময়মনসিংহ/টাঙ্গাইল/নেত্রকোণা/জামালপুর পওর বিভাগ, বাপাউবো, ময়মনসিংহ/টাঙ্গাইল/নেত্রকোণা/জামালপুর।
- ১৩। নির্বাহী প্রকৌশলী, কিশোরগঞ্জ পানি উন্নয়ন বিভাগ, বাপাউবো, কিশোরগঞ্জ।
- ১৪। অফিস কপি।

ALMunir
30.06.24

হিসাবরক্ষণ কর্মকর্তা
আঞ্চলিক হিসাব কেন্দ্র
বাপাউবো, ময়মনসিংহ।

৭/৪/২৪
30/06
24

৬/৪/২৪
30/06/24

আঞ্চলিক হিসাব কেন্দ্র, বাপাউবো, ময়মনসিংহ

প্রাচ্যের নাম “জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাঁকেনদহ ও বালিছুরি এর বগুড়া জেলার সহিয়াকান্দি উপজেলাধীন জামখল এলাকা যখন নদীর তাকন হতে ব্রহ্ম” শীর্ষক প্রবন্ধ

প্রকল্পের কোড নম্বর: ২২৪৩১৪১০০

টাকা

[illegible][illegible]

বিত্তারিত বিতরণ এবং ব্যয়ের প্রতিবেদন

২০২৩-২৪

মন্ত্রণালয়/বিভাগ ১৪৭ - পানি সম্পদ মন্ত্রণালয়

(অংকনমূল টাকায়)

প্রাতিষ্ঠানিক কোড	পরিচালন ইউনিট	মাঠ অফিস	অর্থনৈতিক কোড	বিবরণ	অনুমোদিত			অননুমোদিত	
					বিতরণ	প্রত্যাহার	মোট	প্রকৃত ব্যয়	অবশিষ্ট

১৪৭০১

সচিবালয়, পানি সম্পদ মন্ত্রণালয়

২২৪৩১৪১০০

* জামালপুর জেলার বাহারপাড়া উপজেলাধীন পাকেরদহ ও বাদিপুরি এবং বগুড়া জেলার সারিলাকাশি উপজেলাধীন জামাল এলাকা

২২৪৩১৪১০০০০০০০০

জামালপুর জেলার বাহারপাড়া উপজেলাধীন পাকেরদহ ও বাদিপুরি এবং বগুড়া জেলার সারিলাকাশি উপজেলাধীন জামাল এলাকা বহুলা নদীর

৩১১১ নদী বহুলা ও বৈকুণ্ঠ

৩১১১৩৩২ সামান্য ভাতা ২,৪০,০০০ ০ ২,৪০,০০০ ১,৪৭,৪০০ ৯২,৬০০

উপমোট- নদী বহুলা ও বৈকুণ্ঠ : ২,৪০,০০০ ০ ২,৪০,০০০ ১,৪৭,৪০০ ৯২,৬০০

৩২৪৩ সেন্ট্রাল, অয়েল ও স্ট্রিক্ট

৩২৪৩১০১ সেন্ট্রাল, অয়েল ও স্ট্রিক্ট ১,৪০,০০০ ০ ১,৪০,০০০ ১,৪৮,৩৯৪ ১,৬০৬

উপমোট- সেন্ট্রাল, অয়েল ও স্ট্রিক্ট : ১,৪০,০০০ ০ ১,৪০,০০০ ১,৪৮,৩৯৪ ১,৬০৬

৩২৪৪ অর্থ ও ব্যয়

৩২৪৪১০১ অর্থ ব্যয় ৫০,০০০ ০ ৫০,০০০ ০ ৫০,০০০

উপমোট- অর্থ ও ব্যয় : ৫০,০০০ ০ ৫০,০০০ ০ ৫০,০০০

৩২৪৫ ফ্রান্স ও মনিয়ারি

৩২৪৫১০১ কম্পিউটার সফটওয়্যার ২৫,০০০ ০ ২৫,০০০ ২৪,৯০০ ১০০

৩২৪৫১০৪ স্ট্যাম্প ও সিগ ১২,০০০ ০ ১২,০০০ ০ ১২,০০০

উপমোট- ফ্রান্স ও মনিয়ারি : ৩৭,০০০ ০ ৩৭,০০০ ২৪,৯০০ ১২,১০০

৩২৪৭ সেন্ট্রাল সেকা, সামান্য ও বিশেষ স্বত্ব

৩২৪৭১০৪ জরিপ ৬,০০,০০০ ০ ৬,০০,০০০ ৫,৯৭,১৪৪ ২,৮৪৬

উপমোট- সেন্ট্রাল সেকা, সামান্য ও বিশেষ স্বত্ব : ৬,০০,০০০ ০ ৬,০০,০০০ ৫,৯৭,১৪৪ ২,৮৪৬

৩২৪৮ মেমোরিয়াল ও স্মরণক

৩২৪৮১০১ মেমোরিয়াল ১,১০,০০০ ০ ১,১০,০০০ ১,১১,১০০ ১,২০০

উপমোট- মেমোরিয়াল ও স্মরণক : ১,১০,০০০ ০ ১,১০,০০০ ১,১১,১০০ ১,২০০

৪১১১ ভবন ও স্থাপত্যসমূহ

৪১১১৩২১ বাই ১০৪৮৪,৬৫,০০০ ০ ১০৪৮৪,৬৫,০০০ ১০৪৮৪,৬৫,০০০ ০

উপমোট- ভবন ও স্থাপত্যসমূহ : ১০৪৮৪,৬৫,০০০ ০ ১০৪৮৪,৬৫,০০০ ১০৪৮৪,৬৫,০০০ ০

৪১১২ যন্ত্রপাতি ও সরঞ্জামাদি

৪১১২২০২ কম্পিউটার ও আনুষঙ্গিক ৮৫,০০০ ০ ৮৫,০০০ ৮৪,৯০০ ১০০

উপমোট- যন্ত্রপাতি ও সরঞ্জামাদি : ৮৫,০০০ ০ ৮৫,০০০ ৮৪,৯০০ ১০০

৪১১৩ অন্যান্য স্থায়ী সম্পদ

৪১১৩১০২ যক্ষ, শস্য ও উদ্ভিদসম্পদ ১,০০,০০০ ০ ১,০০,০০০ ১,০০,০০০ ০

উপমোট- অন্যান্য স্থায়ী সম্পদ : ১,০০,০০০ ০ ১,০০,০০০ ১,০০,০০০ ০

মোট : ১০৪৯৯,৫০,০০০ ০ ১০৪৯৯,৫০,০০০ ১০৪৯৯,১৮,৯৪৮ ১,৬১,০৫২

বিত্তায়িত বিভরণ এবং ব্যয়ের প্রতিবেদন

২০২৩-২৪

মহাপালয়/বিভাগ ১৪৭ - পানি সম্পদ মহাপালয়

(অংকসমূহ টাকায়)

প্রাতিষ্ঠানিক কোড	পরিচালন ইউনিট	মাঠ অফিস	অর্থনৈতিক কোড	বিবরণ	অনুমোদিত					অননুমোদিত	
					বিতরণ	প্রত্যাহার	মোট	প্রকৃত ব্যয়	অবশিষ্ট	বিতরণ	প্রত্যাহার
মোট- * জালাপাশুর জেলার সাধারণ উপজেলায় পাকেরদহ ও					১০৪১৯,৪০,০০০	০	১০৪১৯,৪০,০০০	১০৪১৭,১৮,১৪৮	১,৪১,০৪২		
বাগিচুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলায়											
আমকল এলাকা বগুড়া নদীর তীরে তালুক বতে রক্ষা প্রকল্প (১ম											
সংশোধিত) (০১/০৪/২০২০ - ৩০/০৬/২০২৪) অনুমোদিত :											
মোট- সচিবালয়, পানি সম্পদ মহাপালয় :					১০৪১৯,৪০,০০০	০	১০৪১৯,৪০,০০০	১০৪১৭,১৮,১৪৮	১,৪১,০৪২		
মোট- পানি সম্পদ মহাপালয় :					১০৪১৯,৪০,০০০	০	১০৪১৯,৪০,০০০	১০৪১৭,১৮,১৪৮	১,৪১,০৪২		

১
বিত্তারিত বিতরণ এবং ব্যয়ের প্রতিবেদন

২০২৪-২৫

মন্ত্রণালয়/বিভাগ ১৪৭ - পানি সম্পদ মন্ত্রণালয়

(অংকসমূহ টাকায়)

প্রাতিষ্ঠানিক কোড	পরিচালন ইউনিট	মাঠ অফিস	অর্থনৈতিক কোড	বিবরণ	অনুমোদিত					অননুমোদিত	
					বিতরণ	প্রত্যাহার	মোট	প্রকৃত ব্যয়	অবশিষ্ট	বিতরণ	প্রত্যাহার

১৪৭০১

সচিবালয়, পানি সম্পদ মন্ত্রণালয়

২২৪৩১৪১০০

জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিঙ্গুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা

২২৪৩১৪১০০০০০০০০

জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও বালিঙ্গুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন জামখল এলাকা যমুনা নদীর

৩১১১ নগদ মজুরি ও বেতন

৩১১১৩৩২ সম্মানী ভাতা

২,০০,০০০

০

২,০০,০০০

২,০০,০০০

০

উপমোট- নগদ মজুরি ও বেতন :

২,০০,০০০

০

২,০০,০০০

২,০০,০০০

০

৪১১১ ভবন ও স্থাপনাসমূহ

৪১১১৩২১ ঝাঁক

১০১৯৮,০০,০০০

০

১০১৯৮,০০,০০০

৯৩৪৪,৬২,৪৮৬

৮৫৩,৩৭,৫১৪

উপমোট- ভবন ও স্থাপনাসমূহ :

১০১৯৮,০০,০০০

০

১০১৯৮,০০,০০০

৯৩৪৪,৬২,৪৮৬

৮৫৩,৩৭,৫১৪

মোট : ১০২০০,০০,০০০

০

১০২০০,০০,০০০

৯৩৪৪,৬২,৪৮৬

৮৫৩,৩৭,৫১৪

মোট- জামালপুর জেলার মাদারগঞ্জ উপজেলাধীন পাকেরদহ ও

০

১০২০০,০০,০০০

৯৩৪৪,৬২,৪৮৬

৮৫৩,৩৭,৫১৪

বালিঙ্গুরি এবং বগুড়া জেলার সারিয়াকান্দি উপজেলাধীন

জামখল এলাকা যমুনা নদীর ভাঙ্গন হতে রক্ষা প্রকল্প (১ম

সংশোধিত) (০১/০৪/২০২০ - ৩০/০৬/২০২৫) অনুমোদিত :

মোট- সচিবালয়, পানি সম্পদ মন্ত্রণালয় : ১০২০০,০০,০০০

০

১০২০০,০০,০০০

৯৩৪৪,৬২,৪৮৬

৮৫৩,৩৭,৫১৪

মোট- পানি সম্পদ মন্ত্রণালয় : ১০২০০,০০,০০০

০

১০২০০,০০,০০০

৯৩৪৪,৬২,৪৮৬

৮৫৩,৩৭,৫১৪

